

Appendix A Construction Programme

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014			2015	
							Oct	Nov	Dec	Jan	Feb
3-Month Rolling Programme 2014-10-21											
Key Dates (Contractual)											
KD-0010	Commencement of Works	0	0	31-Jul-13 A							
Dependent Milestones from Other Contracts											
MS-0100	Completion of Temporary Vehicular Bridge by C2 Contractor	0	0		31-Dec-14*	-99				◆ Completion of Temporary Vehicular Bridge by C	
Major Milestones and Events											
MS-2000A1	T1a: TTA to shift FLHS SB eastward to the widened pavement (shift 1st lanes)	2	2	01-Nov-14*	02-Nov-14	7				■ T1a: TTA to shift FLHS SB eastward to the widened pavement (shift 1st lanes)	
MS-2000A2	T1b: TTA to shift FLHS SB eastward to the widened pavement (shift 2nd lanes)	2	2	06-Dec-14*	07-Dec-14	7				■ T1b: TTA to shift FLHS SB eastward to the widened pavement (shift 2nd la	
MS-2000A3	T1c: TTA to shift FLHS SB eastward to the widened pavement (shift 3rd lanes)	2	2	10-Jan-15*	11-Jan-15	7				■ T1c: TTA to shift FLHS SB eastward	
Major Procurement & Delivery											
Water Supply Pipeworks											
MM-1050	DN450 DI pipe and pipe fittings	60	7	21-Jun-14 A	28-Oct-14	174				DN450 DI pipe and pipe fittings, DN450 DI pipe and pipe fittings	
MM-1060	E&M equipment for the re-provisioned WSD Valve Control House	60	60	21-Oct-14	31-Dec-14	5				E&M equipment for the re-provisioned WSD V	
Precast Bridge Segment Lifting Frames and Precast Yard											
MM-2020	Procurement and fabrication of lifting frame	105	0	05-May-14 A	27-Sep-14 A					Procurement and fabrication of lifting frame	
MM-2040	Deliver to Site and assembly works	44	27	28-Sep-14 A	20-Nov-14	30				Deliver to Site and assembly works, Deliver to S	
MM-2050	Certification of lifting frame	6	6	21-Nov-14	27-Nov-14	30				Certification of lifting frame	
Design and Submissions											
Statutory Approval											
PRE-1040	Submission & approval of temporary works on nullah for construction of pad footing of Bridge E - DSD	40	7	11-Sep-14 A	28-Oct-14	29				Submission & approval of temporary works on nullah for construction of pad	
PRE-1220	Consent for construction of noise barrier (NB1a) within WSD Tau Pass Restricted Zone - WSD	45	7	09-Apr-14 A	28-Oct-14	31				Consent for construction of noise barrier (NB1a) within WSD Tau Pass Restricted Zone - WSD, Consent for constructio	
PRE-1500	Confirmation of Noise Barrier Footing Design for NB71 (CH7150 to CH7290)	70	14	17-Apr-14 A	05-Nov-14	1412				Confirmation of Noise Barrier Footing Design for NB71 (CH7150 to CH7290), Confirmation of Noise Barrier Fo	
PRE-1260	Approval of Water Mains Alignment beside Fanling Highway (CH7380-7925) (incl. Twin DN1400, DN1200, DN600, DN2300) - WSD	45	14	19-Mar-14 A	05-Nov-14	152				Approval of Water Mains Alignment beside Fanling Highway (CH7380-7925) (incl. Twin DN1400, DN1200, DN6	
PRE-1230B	Consent for installation of bored pile within 30m from WSD Tau Pass Restricted Zone -WSD	90	36	15-Jan-14 A	01-Dec-14	12				Consent for installation of bored pile within 30m from WSD Tau Pass Restricted Z	
PRE-1210	Consent for Dong Jiang watermians connection for DN1400 - WSD	0	0		02-Jan-15*	0				◆ Consent for Dong Jiang watermians connecti	
Method Statement and Design (Major) Approved by AECOM											
PRE-2020	Submission of noise barrier design for absorptive panels, transparent panels and associated fixing details	60	30	11-Mar-14 A	24-Nov-14	181				Submission of noise barrier design for absorptive panels, transparent panels and associat	
Contractor's Alternative Design (AD) Submission & Approval											
PRE-4290	Portal Beam Design Package 2 (AD3)	5	0	23-Aug-14 A	30-Sep-14 A					Portal Beam Design Package 2 (AD3)	

Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014					2015						
							Oct	Nov	Dec	Jan	Feb							
PRE-4220	Pier Design Package B (AB6-AB11)	43	7	28-Nov-13 A	28-Oct-14	-28												
PRE-4260	Pier Design Package F (AD8-AD13)	50	7	20-Jan-14 A	28-Oct-14	23												
PRE-4280	Portal Beam Design Package 2 (AB7/AD9/AC12, AB8, AD11)	38	7	23-Aug-14 A	28-Oct-14	3												
PRE-4340B	Superstructure Design Package 8 for Bridge D2 (AD6-AD8)	56	37	30-Jul-14 A	02-Dec-14	239												
PRE-4340A	Superstructure Design Package 4 for Bridge D1 (AD1-AD5)	110	38	07-May-14 A	03-Dec-14	177												
PRE-4310D	Superstructure Design Package 6 for Bridge A4 (AA14-AA18)	108	44	16-May-14 A	10-Dec-14	104												
PRE-4310A	Superstructure Design Package 9 for Bridge A1 (AA1-AA5)	118	54	16-May-14 A	22-Dec-14	355												
PRE-4310C	Superstructure Design Package 3 for Bridge A3 (AA10-AA13)	158	64	04-Apr-14 A	06-Jan-15	94												
PRE-4320A	Superstructure Design Package 11 for Bridge B1 (AB1-AB6)	73	73	21-Oct-14*	16-Jan-15	325												
PRE-4310B	Superstructure Design Package 10 for Bridge A2 (AA6-AA9)	154	90	16-May-14 A	05-Feb-15	458												
PRE-4330A	Superstructure Design Package 2 for Bridge C1 (AC1-AC5)	196	96	28-Mar-14 A	12-Feb-15	98												
PRE-4320B	Superstructure Design Package 7 for Bridge B2 (AB7-AB12)	196	96	21-May-14 A	12-Feb-15	8												
PRE-4340C	Superstructure Design Package 5 for Bridge D3 (AD9-AD14)	196	96	07-May-14 A	12-Feb-15	37												
Temporary Traffic Arrangement (TTA) Submission and Approval																		
TTA for Tai Wo Service Road East																		
PRE-6220	TTA submission & approval - Scheme ER2 (shifting TWSR East westward towards Fanling Highway for pipe laying works)	30	30	21-Oct-14*	24-Nov-14	71												
PRE-6210	TTA submission & approval - Scheme ER1 (shifting TWSR East to Access Road A)	20	20	22-Dec-14*	16-Jan-15	1353												
Section IA & IB - Fanling Highway Widening (KD-1 & KD-2)																		
Fanling Highway South Portion between CH6935 and CH7470																		
Fanling Highway Zone 1 between CH6935 and CH7130 (within SBZ2)																		
At-Grade Roadworks (195m)																		
FHW-1160	Road Formation, Road Drainage, Kerb and Pavement (Eastern Side)	48	10	31-Jul-14 A	31-Oct-14	6												
FHW-1110*	Pipe Laying - DN1200 Watermains (CHC) across Fanling Highway (total 80m for 2 shafts)	275	56	09-Jun-14 A	24-Dec-14	722												
FHW-1150*	Pipe Laying - DN1200 Watermains (CHC) along Fanling Highway (80m long, 4m depth)	182	176	20-Feb-14 A	30-May-15	722												
Fanling Highway Zone 2 between CH7130 and CH7290																		
At-Grade Roadworks (160m)																		
FHW-2120*	Pipe Laying - Twin DN1400 Watermains (CHE & G) along Fanling Highway (44m long, 6m depth)	85	22	09-Jul-14 A	14-Nov-14	299												
FHW-2110B	Noise Barrier NB71 - Footing adjacent to SB lane (96m) (affected due to design change)	128	154	26-Jul-14 A	04-May-15	102												
FHW-2130*	Pipe Laying - DN1200 & DN600 Watermains (CHB & CHC) along Fanling Highway (183m long, 4m depth)	95	249	26-May-14 A	26-Aug-15	486												



- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- Milestone
- Project Baseline Bar

CEDD Contract No. CV/2012/09

Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3

3-Month Rolling Programme

3MPR015

Page 2 of 9

23-Oct-14

3-Month Rolling Programme updated to 2014-10-21

Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014					2015					
							Oct	Nov	Dec	Jan	Feb						
Fanling Highway Zone 3 between CH7290 and CH7380																	
At-Grade Roadworks (130m)																	
FHW-3130	Noise Barrier NB71 - Footing adjacent to SB lane (130m) Including pile cap	109	84	23-May-14 A	29-Jan-15	144										Noise Barrier	
FHW-3150*	Pipe Laying - DN600, DN1200 Watermains (CHB & CHC) along Fanling Highway (90m long, 3m depth)	150	429	07-Jun-14 A	11-Apr-16	414											
Fanling Highway Zone 4 between CH7380 and CH7470																	
At-Grade Roadworks (90m)																	
FHW-4120*	Pipe Laying - Twin DN1400 Watermains (CHE & CHG) along Fanling Highway (90m long, 3m depth)	155	155	06-Nov-14	21-May-15	152											
Miscellaneous Works for Facilitating Traffic Diversion of Fanling Highway																	
FHW-M-1010	Permanent Road Formation with 1 lanes width between CH7130 and CH7380 (Eastern Side)	62	10	13-Jul-14 A	31-Oct-14	6										Permanent Road Formation with 1 lanes width between CH7130 and CH7380 (Eastern Side), Permanent Road For	
FHW-M-1020	Permanent Road Formation with 2 lanes width between CH7130 and CH7380 (Eastern Side)	29	29	03-Nov-14	05-Dec-14	6										Permanent Road Formation with 2 lanes width between CH7130 and CH7380	
FHW-M-1030	Permanent Road Formation with 3 lanes width between CH7130 and CH7380 (Eastern Side)	26	26	08-Dec-14	09-Jan-15	6										Permanent Road Formation with 3 lanes	
FHW-M-1000	Demolition of Central Barrier & Make Good of Road Pavement for further Traffic Diversion	30	30	12-Jan-15	14-Feb-15	6											
Fanling Highway North Portion between CH7470 and CH7925																	
Fanling Highway Zone 5 between CH7470 and CH7600 (Provision of Kiu Tau Footbridge)																	
Kiu Tau Footbridge Reprovision (East)																	
FHW-5000B	KT-AB2 - Piling Works (4 nos of Pile)	20	20	21-Oct-14	12-Nov-14	96										KT-AB2 - Piling Works (4 nos of Pile)	
FHW-5000D	KT-P3 - Piling Works (8 nos of Pile)	40	40	13-Nov-14	31-Dec-14	96										KT-P3 - Piling Works (8 nos of Pile)	
FHW-5000A	KT-AB1 - Piling Works (12 nos of Pile)	60	60	21-Oct-14	31-Dec-14	96										KT-AB1 - Piling Works (12 nos of Pile)	
FHW-5000E	KT-P4 - Piling Works (8 nos of Pile)	40	40	02-Jan-15	17-Feb-15	96											
FHW-5010B	KT-AB2 - Pile Cap & Abutment	105	105	13-Nov-14	25-Mar-15	291											
FHW-5010D	KT-P3 - Pile Cap & Pier	75	75	02-Jan-15	10-Apr-15	281											
FHW-5010A	KT-AB1 - Pile Cap & Abutment	105	105	02-Jan-15	16-May-15	251											
Fanling Highway Zone 7 between CH7660 and CH7925																	
At-Grade Roadworks (265m)																	
FHW-7100	Site Formation, Preparation Works & Tree Transplant	127	75	30-Aug-13 A	19-Jan-15	309										Site Formation, Preparat	
Section II - Remainder of the Works (KD-3)																	
WSD Works																	
DN600 Water Mains (CHB)																	
WB-1000	Pipe Laying - CHB 0 - 153 (DN600) near Fanling Highway S/B (FHW: CH7130-7290), 153m long (common trench with NB)	95	35	26-May-14 A	29-Nov-14	700											

Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	







Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014					2015	
							Oct	Nov	Dec	Jan	Feb		
WB-0100	Temporary Local Diversion for DN600 near Abutment AD1	80	75	25-Sep-14 A	19-Jan-15	565	Temporary Local D						
WB-1080	Pipe Laying - CHB 700 - 756 (DN600) near Realigned TWSR East (along Roundabout), 56m long & GL	35	35	02-Jan-15*	11-Feb-15	19							
DN1200 Water Mains (CHC)													
WC-1040	Receiving Pit for Twins DN1200 (CHC)	50	0	09-Jun-14 A	25-Sep-14 A		Receiving Pit for Twins DN1200 (CHC)						
WC-1030A	Excavation - CHC 100 - 155 (DN1200) across Fanling Highway by Trenchless Method, 110m long for 2 shafts	169	10	19-Sep-14 A	31-Oct-14	722							
WC-1030B	Pipe Laying - CHC 100 - 155 (DN1200) across Fanling Highway & associated Grouting Works	46	46	01-Nov-14	24-Dec-14	722	Pipe Laying - CHC 100 - 155 (DN1200) across Fanling						
WC-1140	Pipe Laying - CHC 980 - 1030 (DN1200) near Realigned TWSR East (along Roundabout), 50m long & GL	35	35	02-Jan-15*	11-Feb-15	19							
WC-1050A	Pipe Laying - CHC 155 - 235 (DN1200) near Fanling Highway S/B (FHW: CH6935-7130), 50m long, 4m depth	120	120	27-Dec-14	30-May-15	722							
DN1400 Water Mains (CHD)													
WD-2020	Water Sampling	7	0	20-Sep-14 A	24-Sep-14 A		Water Sampling						
WD-2030	Connection to Existing Mains	1	0	25-Sep-14 A	11-Oct-14 A		Connection to Existing Mains						
Twin DN1400 Water Mains (CHE & CHG)													
WE-1000	Pipe Laying - CHE & CHG 0 - 45 (Twins DN1400) near Fanling Highway S/B (FHW: CH7130-7290), 45m long & 6m depth	85	22	09-Jul-14 A	14-Nov-14	299	Pipe Laying - CHE & CHG 0 - 45 (Twins DN1400) near Fanling High						
WE-1020	Pipe Laying - CHE & CHG 135 - 225 (Twins DN1400) near Fanling Highway S/B (FHW: CH7380-7470), 90m long & 3m depth	155	155	06-Nov-14	21-May-15	152							
DN2300 Water Mains and Leakage Collection System (CHJ & CHKA/CHK)													
WJ-1050	Pipe Laying - CHJ 200 - 292 (DN2300) near Realigned TWSR East (along Access Road A), 92m long & GL	97	57	01-Sep-14 A	27-Dec-14	57	Pipe Laying - CHJ 2						
WJ-1030	Pipe Laying - CHJ 100 - 170 (DN2300) near Realigned TWSR East, 70m long & 3m depth	75	75	04-Nov-14	02-Feb-15	14	Pipe Lay						
WJ-1000	Implementation of TTA - Scheme EX2 (Shifting TWSRE toward newly formation area beside Fanling Highway)	35	35	20-Dec-14	02-Feb-15	14	Impleme						
WJ-1100	DN300 Washout at CHJ 212	65	65	21-Nov-14	07-Feb-15	149	DN						
WJ-1020B	Pipe Laying - CHKA 0 - 73 (DN1400) near Realigned TWSR East, 73m long & 4m depth	65	65	06-Jan-15	11-Mar-15	4							
Kau Lung Hang Valve Control & Telemetry House Re provision													
VCTH-1000	Civil Works Construction	75	0	15-Aug-14 A	18-Oct-14 A		Civil Works Construction						
VCTH-1010	BS and E&M Works	90	90	02-Jan-15	28-Apr-15	5							
Existing Nam Wa Po Trunk Sewage Pumping Station (PST3)													
PS-1000	Demolition of Existing Boundary Wall of Pumping Station (PST3)	25	25	05-Jan-15*	02-Feb-15	841	Demolitic						
Stage 1A - Realignment of Tai Wo Service Road West (KD-7)													
TWSRW Zone 1 between CH100 and CH155													
At-Grade Roadworks													
TWSRW-1120	Noise Barrier NB4 - Footing adjacent to Realigned TWSR West (70m)	85	0	12-Apr-14 A	23-Sep-14 A		Noise Barrier NB4 - Footing adjacent to Realigned TWSR West (70m)						

Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014				
							Oct	Nov	Dec	Jan	Feb
TWSRW-1130	Laying of Southern Trunk Sewer (West)	95	11	23-Apr-14 A	01-Nov-14	83	Laying of Southern Trunk Sewer (West), Laying of Southern Trunk Sewer (West)				
TWSRW-1100	Tree Survey, Tree Felling and Transplanting	81	32	16-Oct-13 A	26-Nov-14	72	Tree Survey, Tree Felling and Transplanting, Tree Survey, Tree Felling and Transplanting				
TWSRW-1150	Installation of Cable Ducts for Utilities Diversion Works at Zone 1 & Zone 2 (Approx. 100m) (by utilities undertakers)	167	167	22-Oct-14*	06-Apr-15	96					
TWSRW-1160	Road Formation, Road Drainage, Kerb, Planter & Pavement	286	286	22-Oct-14	12-Oct-15	79					
TWSRW Zone 2 between CH155 and CH280											
At-Grade Roadworks											
TWSRW-2120	Road Formation, Road Drainage, Kerb, Planter and Pavement	337	333	16-Oct-14 A	05-Dec-15	33					
TWSRW Zone 3 between CH280 and CH315											
At-Grade Roadworks											
TWSRW-3100	Noise Barrier NB1a - Footing adjacent Realigned TWSR West (31m)	80	80	29-Oct-14	02-Feb-15	31	Noise Bar				
TWSRW Zone 4 between CH315 and CH376											
Construction of Bridge E											
TWSRW-4030B	Bored Pile Works for AE2 (4 nos.)	60	0	25-Jul-14 A	23-Sep-14 A		Bored Pile Works for AE2 (4 nos.)				
TWSRW-4040B	Pile Test for AE2	7	0	03-Oct-14 A	20-Oct-14 A		Pile Test for AE2				
TWSRW-4000B	CLP Overhead 11KV Cable Diversion at Area B (Phase 2)	140	23	04-Nov-13 A	15-Nov-14	25	CLP Overhead 11KV Cable Diversion at Area B (Phase 2), CLP Overhead 11 KV Cable Diversion at				
TWSRW-4050B	Pile Cap for AE2	45	38	13-Oct-14 A	03-Dec-14	43	Pile Cap for AE2, Pile Cap for AE2				
TWSRW-4010A	Pre-Drilling for AE1 (refer to conditions of WSD)	12	12	02-Dec-14*	15-Dec-14	12	Pre-Drilling for AE1 (refer to conditions of WSD)				
TWSRW-4060	Construction of Temporary Support at DSD nullah (Work in dry season)	45	45	01-Nov-14	23-Dec-14	26	Construction of Temporary Support at DSD nullah (Work				
TWSRW-4030A	Bored Pile Works for AE1	65	65	16-Dec-14	11-Mar-15	12					
TWSRW-4070	In-situ Casting for Bridge Segment (North Bay & Middle Bay)	110	110	24-Dec-14	16-May-15	26					
TWSRW Zone 5 between CH376 and CH520											
Construction of Retaining Structures											
TWSRW-5050D	Construction of Remaining Portion of Bored Pile Wall at formation level	85	31	02-Sep-14 A	25-Nov-14	25	Construction of Remaining Portion of Bored				
TWSRW-5070	Construction of Mass Concrete Wall (FL/RW4)	35	35	26-Nov-14	08-Jan-15	35	Construction of Mass Concrete Wall (
TWSRW-5080	Slope Work incl. 53 nos. Soil Nail for 3SW-C/C898 & 3SW-D/C29	90	90	09-Jan-15	06-May-15	35					
TWSRW-5090	Lagging Wall Construction and Capping Beam	135	135	26-Nov-14	18-May-15	25					
TWSRW Zone 6 between CH520 and CH530											
Box Culvert Extension - BC01											
TWSRW-6070	Inlet structure of the box culvert BC01	60	60	01-Nov-14*	13-Jan-15*	60	Inlet structure of the box culvert				








Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	


Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014					2015				
							Oct	Nov	Dec	Jan	Feb					
TWSRW Zone 7 between CH530 and CH640																
Construction of Retaining Structures																
TWSRW-7010	Slope Cutting and Drainage Channel	235	0	06-Dec-13 A	30-Sep-14 A											
At-Grade Roadworks																
TWSRW-7130	Road Drainage (incl. Zone 6 & Zone 7)	35	35	21-Oct-14	29-Nov-14	21										
TWSRW-7140	Installation of Cable Ducts for Utilities Diversion Works at Area 4 (Approx. 150m) (by utilities undertakers)	251	251	30-Nov-14	07-Aug-15	27										
TWSRW Zone 8 between CH640 and CH695																
Kiu Tau Footbridge Reprvision (West)																
TWSRW-8000	Pre-Drilling Works for Socket H-Pile	45	32	06-Oct-14 A	26-Nov-14	13										
TWSRW-8010	Installation of Socket H-Pile for Proposed Kiu Tau Footbridge (14 nos of Pile)	70	70	27-Nov-14	26-Feb-15	13										
Remainder of the Works																
TWSRW-9010*	Utilities Diversion in Area 1 (along Re-aligned TWSRW CH100 - CH280)	167	167	22-Oct-14	06-Apr-15	96										
TWSRW-9040*	Utilities Diversion in Area 4 (along Re-aligned TWSRW CH530 - CH640)	251	251	30-Nov-14	07-Aug-15	27										
Stage N4A & N4B - Realignment of Tai Wo Service Road East (KD-13 & KD-14)																
TWSRE Zone 1 between CH100 and CH270																
At-Grade Roadworks																
TWSRE-1140*	Pipe laying - DN1400 Watermains (CHKA) along Realigned TWSR East	50	50	06-Jan-15	11-Mar-15	3										
TWSRE Zone 2 between CH270 and CH380																
At-Grade Roadworks																
TWSRE-2020	Retaining Wall Construction for FL/RW6	45	45	21-Oct-14	11-Dec-14	4										
TWSRE Zone 3 between CH380 and CH456																
At-Grade Roadworks																
TWSRE-3020B*	Pipe laying - DN2300 Watermains (CHJ) along Realigned TWSR East	75	75	04-Nov-14	02-Feb-15	14										
Roundabout A, Slip Road and Access Road																
TWSRE-4000	Site Formation, Preparation Works & Tree Transplant	65	12	15-Apr-14 A	03-Nov-14	14										
TWSRE-4050B*	Pipe laying - DN2300 Watermains (CHJ) along Access Road A & Roundabout	91	57	20-Jun-14 A	27-Dec-14	57										
TWSRE-4060	Access Road A - Road Formation, Road Drainage, Kerb, Planter and Pavement	134	59	18-Jul-14 A	30-Dec-14	114										
TWSRE-4040	Slip Road Y (CH100-CH230) - Road Formation, Road Drainage, Kerb, Planter and Pavement	158	132	18-Sep-14 A	02-Apr-15	54										
TWSRE-4050A*	Pipe laying - DN600 & DN1200 Watermains (CHB & CHC) along Access Road A & Roundabout	107	107	02-Jan-15	19-May-15	19										

-  Actual Work
-  Remaining Work
-  Summary Bar
-  Critical Remaining Work
-  Milestone
-  Project Baseline Bar

Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014				2015		
							Oct	Nov	Dec	Jan	Feb		
Stage 1C - Viaduct Structure & TCSS Civil Provisions (KD-9)													
Preliminaries													
B-5000	Provide a Temporary Cycle Track (Scheme 1)	27	0	22-May-14 A	05-Oct-14 A		Provide a Temporary Cycle Track (Scheme 1)						
B-1000A	ADMS Installation inside MTRCL Railway (for pier AD11, AD12, AB10)	14	14	21-Oct-14*	05-Nov-14	21	ADMS Installation inside MTRCL Railway (for pier AD11, AD12, AB10)						
B-1010A	Demonstration to MTRCL (for pier AD11, AD12, AB10)	1	1	06-Nov-14	06-Nov-14	21	Demonstration to MTRCL (for pier AD11, AD12, AB10)						
B-2030	Completion of CLP Overhead 11KV Cable Diversion at Area B (Phase 2)	0	0		15-Nov-14	51	Completion of CLP Overhead 11KV Cable Diversion at Area B (Phase 2)						
B-1020A	Base-line Monitoring (for pier AD11, AD12, AB10)	10	10	07-Nov-14	18-Nov-14	21	Base-line Monitoring (for pier AD11, AD12, AB10)						
B-4020	Erection of Catch Fence at DSD Maintenance Access	37	30	13-Oct-14 A	24-Nov-14	16	Erection of Catch Fence at DSD Maintenance Access, Erection of Catch Fence at						
B-9000	Trial Operation (AC8 - Early Start on 26 Nov 14)	60	60	06-Jan-15	23-Mar-15	0	Trial Operation (AC8 - Early Start on 26 Nov 14)						
Foundation & Pier Construction													
Bridge A													
BA-04-1010	Pier AA4 - Pile Test	7	0	30-Aug-14 A	04-Oct-14 A		Pier AA4 - Pile Test						
BA-18-1010	Pier AA18 - Pile Test	7	0	08-Sep-14 A	06-Oct-14 A		Pier AA18 - Pile Test						
BA-02-2000	Pier AA2E - Piling Works	12	0	17-Sep-14 A	10-Oct-14 A		Pier AA2E - Piling Works						
BA-03-1010	Pier AA3 - Pile Test	7	7	21-Oct-14	28-Oct-14	201	Pier AA3 - Pile Test						
BA-13-1020	Pier AA13 - Pile Cap	30	10	13-Aug-14 A	31-Oct-14	25	Pier AA13 - Pile Cap, Pier AA13 - Pile Cap						
BA-02-2010	Pier AA2E - Pile Test	7	7	27-Oct-14	03-Nov-14	226	Pier AA2E - Pile Test						
BA-14-1020	Pier AA14 - Pile Cap	30	30	16-Oct-14 A	24-Nov-14	9	Pier AA14 - Pile Cap, Pier AA14 - Pile Cap						
BA-13-1030	Pier AA13 - Pier Construction	38	38	06-Nov-14	19-Dec-14	21	Pier AA13 - Pier Construction						
BA-14-1030	Pier AA14 - Pier Construction	30	30	05-Dec-14	12-Jan-15	0	Pier AA14 - Pier Construction						
BA-16-1000	Pier AA16 - Piling Works	12	12	29-Dec-14	12-Jan-15	41	Pier AA16 - Piling Works						
BA-10-1000	Pier AA10 - Piling Works	24	24	13-Jan-15	09-Feb-15	41	Pier AA10 - Piling Works						
Bridge B													
BB-06-1010	Pier AB6 - Pile Test	7	0	19-Jul-14 A	22-Sep-14 A		Pier AB6 - Pile Test						
BB-08-1010A	Pier AB8(P2) - Pile Test	5	0	04-Jul-14 A	13-Oct-14 A		Pier AB8(P2) - Pile Test						
BB-07-1010	Pier AB7 - Pile Test	7	7	13-Sep-14 A	28-Oct-14	17	Pier AB7 - Pile Test, Pier AB7 - Pile Test						
BB-08-1010B	Pier AB8(P1) - Pile Test	7	7	21-Oct-14	28-Oct-14	-58	Pier AB8(P1) - Pile Test						
BB-06-1020A	Pier AB6E - Pile Cap	30	21	10-Oct-14 A	13-Nov-14	-72	Pier AB6E - Pile Cap						
BB-09-1000	Pier AB9 - Piling Works	24	24	23-Oct-14*	19-Nov-14	-35	Pier AB9 - Piling Works						

 俊和建築工程有限公司 CHUN WO CONSTRUCTION & ENGINEERING CO., LTD.	 Actual Work  Remaining Work  Summary Bar  Critical Remaining Work  Milestone  Project Baseline Bar	CEDD Contract No. CV/2012/09 Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3 3-Month Rolling Programme	3-Month Rolling Programme updated to 2014-10-21 <table border="1"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>23-Oct-14</td> <td>Rev.1</td> <td>SL</td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	23-Oct-14	Rev.1	SL													
	Date	Revision	Checked	Approved																			
	23-Oct-14	Rev.1	SL																				
3MPR015	Page 7 of 9	23-Oct-14																					

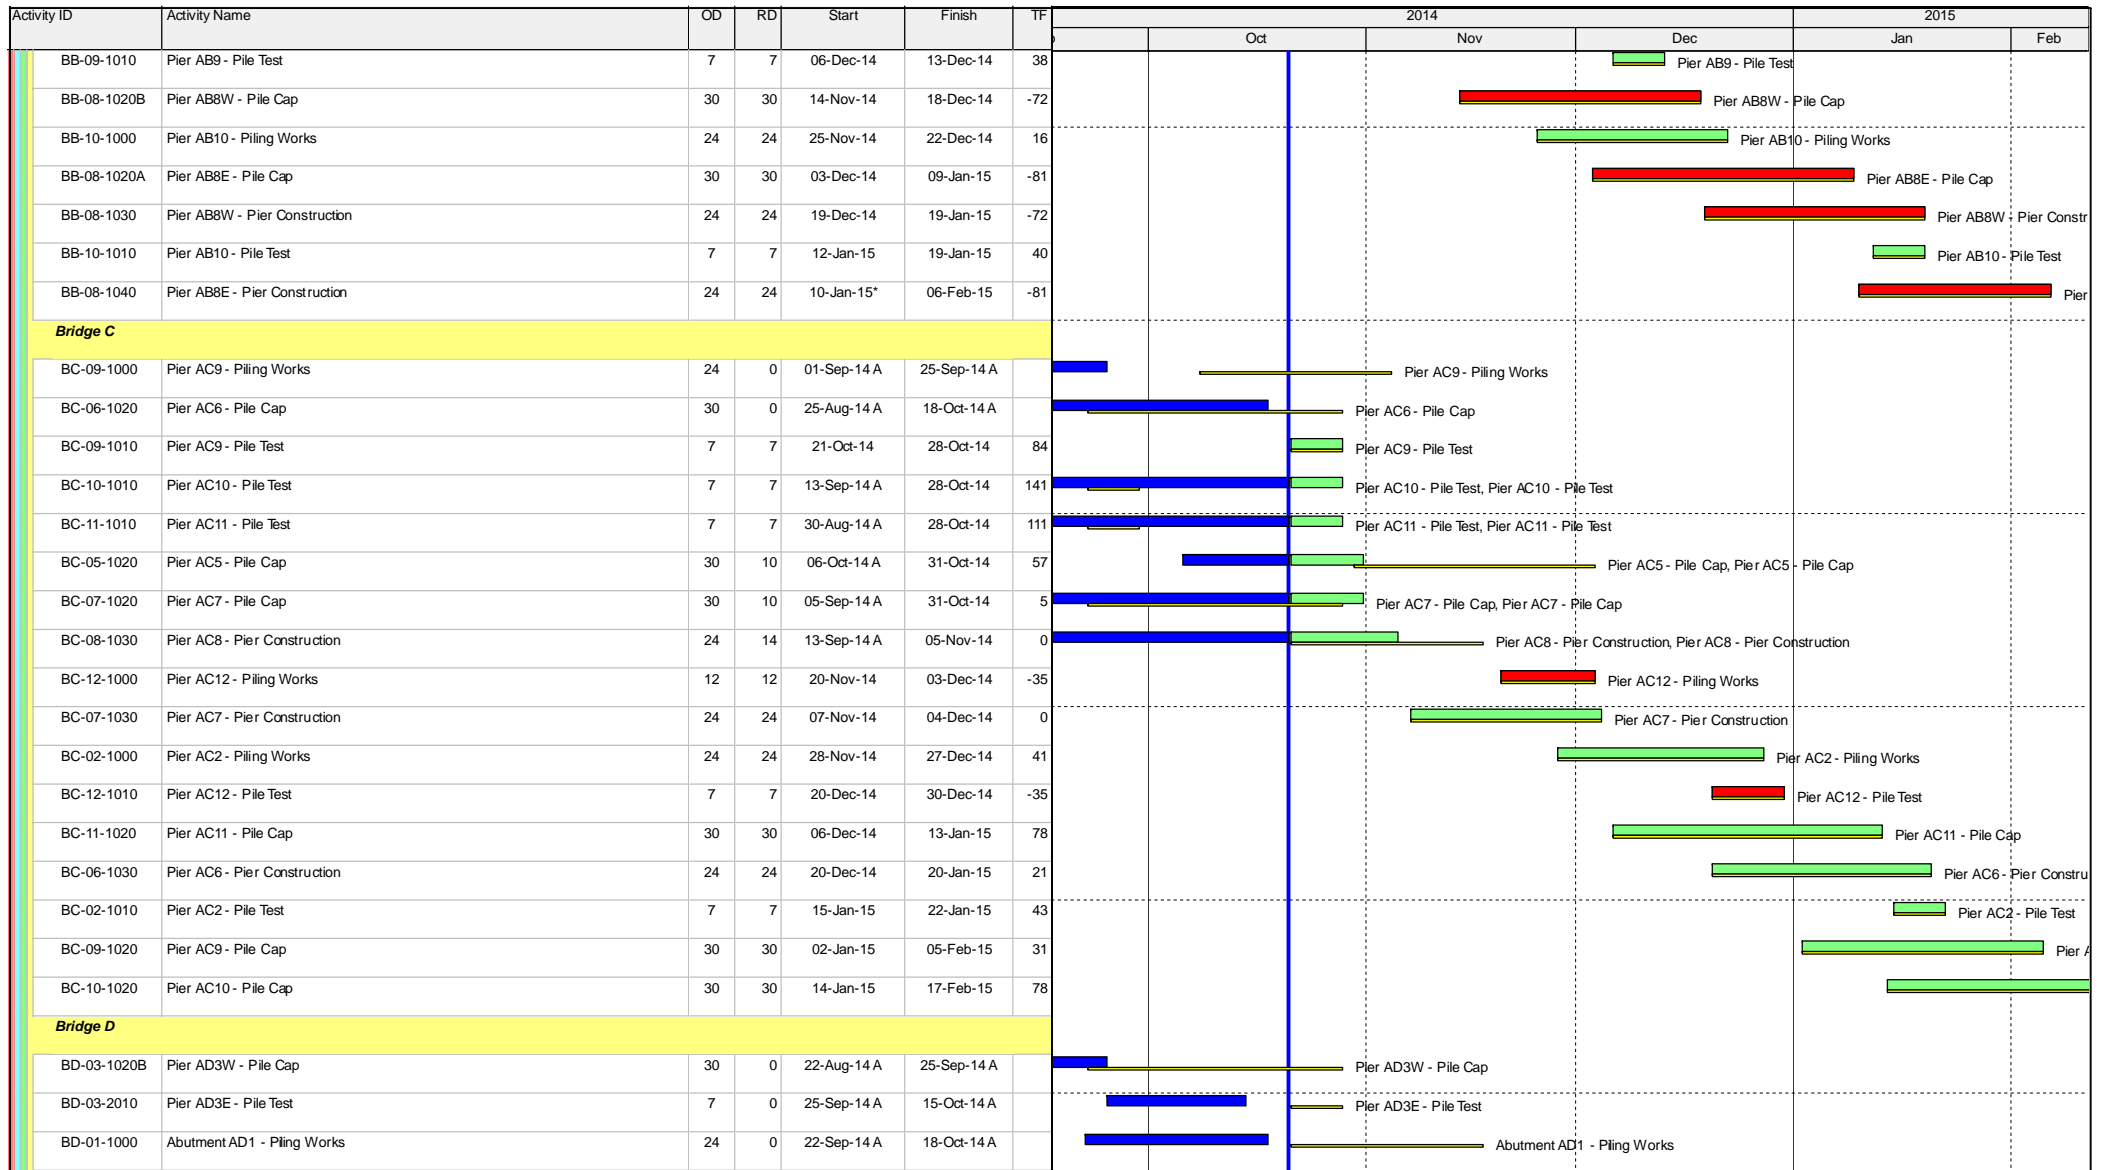

- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- Milestone
- Project Baseline Bar

Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014				2015		
							Oct	Nov	Dec	Jan	Feb		
BD-08-1010	Pier AD8 - Pile Test	7	7	23-Aug-14 A	28-Oct-14	-81	Pier AD8 - Pile Test, Pier AD8 - Pile Test						
BD-03-1030	Pier AD3W - Pier Construction	10	10	27-Oct-14*	06-Nov-14	0		Pier AD3W - Pier Construction					
BD-01-1010	Abutment AD1 - Pile Test	7	7	04-Nov-14	11-Nov-14	537		Abutment AD1 - Pile Test					
BD-10-1000	Pier AD10 - Piling Works	24	24	31-Oct-14*	27-Nov-14	-60		Pier AD10 - Piling Works					
BD-08-1020	Pier AD8 - Pile Cap	30	30	29-Oct-14	02-Dec-14	-81		Pier AD8 - Pile Cap					
BD-03-1020A	Pier AD3E - Pile Cap	30	30	01-Nov-14	05-Dec-14	57		Pier AD3E - Pile Cap					
BD-04-1020	Pier AD4 - Pile Cap	30	30	01-Nov-14	05-Dec-14	67		Pier AD4 - Pile Cap					
BD-10-1010	Pier AD10 - Pile Test	7	7	15-Dec-14	22-Dec-14	-60			Pier AD10 - Pile Test				
BD-06-1020	Pier AD6 - Pile Cap	30	30	25-Nov-14	31-Dec-14	31		Pier AD6 - Pile Cap					
BD-11-1000	Pier AD11 - Piling Works	24	24	23-Dec-14	22-Jan-15	16			Pier AD11 - Piling Works				
BD-10-1020	Pier AD10 - Pile Cap	30	30	23-Dec-14	29-Jan-15	-60			Pier AD10 - Pile Cap				
BD-09-1020	Pier AD9 - Pile Cap	30	30	10-Jan-15	13-Feb-15	-73			Pier AD9 - Pile Cap				
BD-05-1030	Pier AD5 - Pier Construction (Twin Pier)	38	38	13-Jan-15	04-Mar-15	0			Pier AD5 - Pier Construction (Twin Pier)				
Pier Head Construction													
Bridge A													
PA-1130	Pier Head Construction at Pier AA13	35	35	09-Jan-15	18-Feb-15	57			Pier Head Construction at Pier AA13				
Bridge C													
PC-1080	Pier Head Construction at Pier AC8	35	35	22-Nov-14	05-Jan-15	0		Pier Head Construction at Pier AC8					
PC-1070	Pier Head Construction at Pier AC7	35	35	22-Dec-14	03-Feb-15	48		Pier Head Construction at Pier AC7					
Section VI - Works in Portion FH9 (KD-6A)													
Preliminary Preparation Works													
S6-1000	Completion of Temporary Vehicular Bridge by C2 Contractor	0	0		31-Dec-14	20			Completion of Temporary Vehicular Bridge by C2 Contractor				
S6-1020	Site Clearance and Site Formation	14	14	02-Jan-15	17-Jan-15	20			Site Clearance and Site Formation				

Date	Revision	Checked	Approved
23-Oct-14	Rev.1	SL	
