

# Appendix A Construction Programme

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014		2015				
							Dec	Jan	Feb	Mar	Apr		
<b>3-Month Rolling Programme 2014-12-21</b>													
<b>Key Dates (Contractual)</b>													
KD-0010	Commencement of Works	0	0	31-Jul-13 A									
<b>Dependent Milestones from Other Contracts</b>													
MS-0100	Completion of Temporary Vehicular Bridge by C2 Contractor	0	0		31-Dec-14*	-99			◆	Completion of Temporary Vehicular Bridge by C2 Contractor			
<b>Major Milestones and Events</b>													
MS-2000A2	T1b: TTA to shift FLHS SB eastward to the widened pavement (shift 2nd lanes)	1	1	25-Jan-15*	25-Jan-15	8				▮	T1b: TTA to shift FLHS SB eastward to the widened pavement (shift 2nd lanes)		
MS-2000A3	T1c: TTA to shift FLHS SB eastward to the widened pavement (shift 3rd lanes)	1	1	01-Feb-15*	01-Feb-15	9				▮	T1c: TTA to shift FLHS SB eastward to the widened pavement (shift 3rd lanes)		
MS-2000B	T2: TTA to shift FLHS NB & TWSRW eastward	1	1	15-Feb-15*	15-Feb-15	17				▮	T2: TTA to shift FLHS NB & TWSRW eastward		
<b>Major Procurement &amp; Delivery</b>													
<b>Water Supply Pipeworks</b>													
MM-1050	DN450 DI pipe and pipe fittings	60	7	21-Jun-14 A	31-Dec-14	121					DN450 DI pipe and pipe fittings, DN450 DI pipe and pipe fittings		
MM-1060	E&M equipment for the re-provisioned WSD Valve Control House	60	60	22-Dec-14	11-Mar-15	161					E&M equipment for the re-provisioned WSD Valve Control House		
<b>Precast Bridge Segment Lifting Frames and Precast Yard</b>													
MM-2040	Deliver to Site and assembly works	44	2	28-Sep-14 A	23-Dec-14	0					Deliver to Site and assembly works, Deliver to Site and assembly works		
MM-2050	Certification of lifting frame	14	14	24-Dec-14	12-Jan-15	0					Certification of lifting frame		
<b>Design and Submissions</b>													
<b>Statutory Approval</b>													
PRE-1230B	Consent for installation of bored pile within 30m from WSD Tau Pass Restricted Zone -WSD	90	0	15-Jan-14 A	15-Dec-14 A						Consent for installation of bored pile within 30m from WSD Tau Pass Restricted Zone -WSD		
PRE-1210	Consent for Dong Jiang watermians connection for DN1400 - WSD	0	0		02-Jan-15*	0				◆	Consent for Dong Jiang watermians connection for DN1400 - WSD		
PRE-1040	Submission & approval of temporary works on nullah for construction of pad footing of Bridge E - DSD	40	10	11-Sep-14 A	05-Jan-15	-27					Submission & approval of temporary works on nullah for construction of pad footing of Bridge E - DSD, Submis		
PRE-1500	Confirmation of Noise Barrier Footing Design for NB71 (CH7150 to CH7290)	70	14	17-Apr-14 A	09-Jan-15	1359					Confirmation of Noise Barrier Footing Design for NB71 (CH7150 to CH7290), Confirmation of Noise Barr		
PRE-1220	Consent for construction of noise barrier (NB1a) within WSD Tau Pass Restricted Zone - WSD	45	21	09-Apr-14 A	17-Jan-15	162					Consent for construction of noise barrier (NB1a) within WSD Tau Pass Restricted Zone - WSD,		
<b>Method Statement and Design (Major) Approved by AECOM</b>													
PRE-2020	Submission of noise barrier design for absorptive panels, transparent panels and associated fixing details	60	30	11-Mar-14 A	28-Jan-15	128					Submission of noise barrier design for absorptive panels, transparent panels and as		
<b>Temporary Traffic Arrangement (TTA) Submission and Approval</b>													
<b>TTA for Tai Wo Service Road East</b>													
PRE-6210	TTA submission & approval - Scheme ER1 (shifting TWSR East to Access Road A)	20	20	22-Dec-14*	16-Jan-15	1353					TTA submission & approval - Scheme ER1 (shifting TWSR East to Access Road A)		
PRE-6220	TTA submission & approval - Scheme ER2 (shifting TWSR East westward towards Fanling Highway for pipe laying works)	30	30	22-Dec-14*	28-Jan-15	1343					TTA submission & approval - Scheme ER2 (shifting TWSR East westward towards f		

- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- ◆ Milestone
- Project Baseline Bar

Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014		2015			
							Dec	Jan	Feb	Mar	Apr	
<b>Section IA &amp; IB - Fanling Highway Widening (KD-1 &amp; KD-2)</b>												
<b>Fanling Highway South Portion between CH6935 and CH7470</b>												
<b>Fanling Highway Zone 1 between CH6935 and CH7130 (within SBZ2)</b>												
<b>At-Grade Roadworks (195m)</b>												
FHW-1110*	Pipe Laying - DN1200 Watermains (CHC) across Fanling Highway (total 80m for 2 shafts)	275	9	09-Jun-14 A	03-Jan-15	887						
FHW-1150*	Pipe Laying - DN1200 Watermains (CHC) along Fanling Highway (80m long, 4m depth)	182	74	20-Feb-14 A	27-Mar-15	771						
<b>Fanling Highway Zone 2 between CH7130 and CH7290</b>												
<b>At-Grade Roadworks (160m)</b>												
FHW-2120*	Pipe Laying - Twin DN1400 Watermains (CHE & G) along Fanling Highway (44m long, 6m depth)	85	31	09-Jul-14 A	29-Jan-15	252						
FHW-2110B	Noise Barrier NB71 - Footing adjacent to SB lane (96m) (affected due to design change)	128	134	26-Jul-14 A	12-Jun-15	69						
FHW-2200	Noise Barrier NB67 - Mini-Piling adjacent to NB lane (CSD: 36 nos)	108	108	16-Feb-15	07-Jul-15	9						
FHW-2130*	Pipe Laying - DN1200 & DN600 Watermains (CHB & CHC) along Fanling Highway (183m long, 4m depth)	95	229	26-May-14 A	06-Oct-15	453						
<b>Fanling Highway Zone 3 between CH7290 and CH7380</b>												
<b>At-Grade Roadworks (130m)</b>												
FHW-3130	Noise Barrier NB71 - Footing adjacent to SB lane (130m) Including pile cap	109	84	23-May-14 A	13-Apr-15	106						
FHW-3210	Noise Barrier NB69 - Mini-Piling adjacent to NB lane (CSD: 34nos)	68	68	16-Feb-15	18-May-15	140						
FHW-3150*	Pipe Laying - DN600, DN1200 Watermains (CHB & CHC) along Fanling Highway (90m long, 3m depth)	150	429	07-Jun-14 A	15-Jun-16	361						
<b>Fanling Highway Zone 4 between CH7380 and CH7470</b>												
<b>At-Grade Roadworks (90m)</b>												
FHW-4120*	Pipe Laying - Twin DN1400 Watermains (CHE & CHG) along Fanling Highway (90m long, 3m depth)	155	30	15-Oct-14 A	28-Jan-15	253						
<b>Miscellaneous Works for Facilitating Traffic Diversion of Fanling Highway</b>												
FHW-M-1020	Permanent Road Formation with 2 lanes width between CH7130 and CH7380 (Eastern Side)	29	27	10-Nov-14 A	24-Jan-15	6						
FHW-M-1030	Permanent Road Formation with 3 lanes width between CH7130 and CH7380 (Eastern Side)	6	6	26-Jan-15	31-Jan-15	7						
FHW-M-1000	Demolition of Central Barrier & Make Good of Road Pavement for further Traffic Diversion	12	12	02-Feb-15	14-Feb-15	8						
<b>Fanling Highway North Portion between CH7470 and CH7925</b>												
<b>Fanling Highway Zone 5 between CH7470 and CH7600 (Provision of Kiu Tau Footbridge)</b>												
<b>Kiu Tau Footbridge Re-provision (East)</b>												
FHW-5000B	KT-AB2 - Piling Works (4 nos of Pile)	20	0	24-Sep-14 A	27-Nov-14 A							
FHW-5000D	KT-P3 - Piling Works (6 nos of Pile)	40	33	06-Oct-14 A	31-Jan-15	85						



**俊和建築工程有限公司**  
CHUN WO CONSTRUCTION & ENGINEERING CO., LTD.

- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- ◆ Milestone
- Project Baseline Bar

**CEDD Contract No. CV/2012/09**


**Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3**

**3-Month Rolling Programme**

**3MPR017** **Page 2 of 9** **29-Dec-14**

3-Month Rolling Programme updated to 2014-12-21			
Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014				2015				
							Dec	Jan	Feb	Mar	Apr				
FHW-5000A	KT-AB1 - Piling Works (12 nos of Pile)	60	60	29-Sep-14 A	11-Mar-15	58									
FHW-5000C	KT-P2 - Piling Works (6 nos of Pile)	30	75	04-Oct-14 A	28-Mar-15	242									
FHW-5000E	KT-P4 - Piling Works (8 nos of Pile)	40	40	12-Mar-15	02-May-15	58									
FHW-5010B	KT-AB2 - Pile Cap & Abutment	105	105	22-Dec-14	08-May-15	258									
FHW-5010D	KT-P3 - Pile Cap & Pier	75	75	02-Feb-15	12-May-15	255									
FHW-5010A	KT-AB1 - Pile Cap & Abutment	105	105	12-Mar-15	21-Jul-15	198									
<b>Fanling Highway Zone 7 between CH7660 and CH7925</b>															
<b>At-Grade Roadworks (265m)</b>															
FHW-7100	Site Formation, Preparation Works & Tree Transplant	190	74	30-Aug-13 A	27-Mar-15	257									
<b>Section II - Remainder of the Works (KD-3)</b>															
<b>WSD Works</b>															
<b>DN450 Fire Mains (CHA)</b>															
WA-1030	Pipe Laying - CHA260 - 360 (DN450) near Ext. TWSR West, 100m long & 2m depth	65	65	16-Feb-15	14-May-15	18									
<b>DN600 Water Mains (CHB)</b>															
WB-0100	Temporary Local Diversion for DN600 near Abutment AD1	80	33	25-Sep-14 A	31-Jan-15	554									
WB-1000	Pipe Laying - CHB 0 - 153 (DN600) near Fanling Highway S/B (FHW: CH7130-7290), 153m long (common trench with NB)	95	35	26-May-14 A	03-Feb-15	647									
WB-1080	Pipe Laying - CHB 700 - 756 (DN600) near Realigned TWSR East (along Roundabout), 56m long & GL	35	35	02-Jan-15*	11-Feb-15	16									
WB-1090	Pipe Laying - CHB 756 - 849 (DN600) near Realigned TWSR East (along Slip Road A), 93m long & GL	72	72	16-Feb-15	22-May-15	13									
<b>DN1200 Water Mains (CHC)</b>															
WC-1030B	Pipe Laying - CHC 100 - 155 (DN1200) across Fanling Highway & associated Grouting Works	46	9	14-Nov-14 A	03-Jan-15	887									
WC-1140	Pipe Laying - CHC 980 - 1030 (DN1200) near Realigned TWSR East (along Roundabout), 50m long & GL	35	35	02-Jan-15*	11-Feb-15	16									
WC-1050A	Pipe Laying - CHC 155 - 235 (DN1200) near Fanling Highway S/B (FHW: CH6935-7130), 50m long, 4m depth	120	74	29-Oct-14 A	27-Mar-15	771									
WC-1150	Pipe Laying - CHC 1030 - 1123 (DN1200) near Realigned TWSR East (along Slip Road A), 93m long & GL	72	72	16-Feb-15	22-May-15	13									
<b>Twin DN1400 Water Mains (CHE &amp; CHG)</b>															
WE-1020	Pipe Laying - CHE & CHG 135 - 225 (Twins DN1400) near Fanling Highway S/B (FHW: CH7380-7470), 90m long & 3m depth	155	30	15-Oct-14 A	28-Jan-15	253									
WE-1000	Pipe Laying - CHE & CHG 0 - 45 (Twins DN1400) near Fanling Highway S/B (FHW: CH7130-7290), 45m long & 6m depth	85	31	09-Jul-14 A	29-Jan-15	252									
<b>DN2300 Water Mains and Leakage Collection System (CHJ &amp; CHKA/CHK)</b>															
WJ-1010	Pipe Laying - CHJ 0 - 100 (DN2200) near existing TWSR East, 100m long & 6m depth	120	51	13-Oct-14 A	09-Feb-15	189									
WJ-1050	Pipe Laying - CHJ 200 - 292 (DN2300) near Realigned TWSR East (along Access Road A), 92m long & GL	97	45	01-Sep-14 A	14-Feb-15	13									



俊和建築工程有限公司  
CHUN WO CONSTRUCTION & ENGINEERING CO., LTD.

Actual Work

Remaining Work

Summary Bar

Critical Remaining Work

Milestone

Project Baseline Bar

**CEDD Contract No. CV/2012/09**

**Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3**

**3-Month Rolling Programme**

3-Month Rolling Programme updated to 2014-12-21

Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014				2015								
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul					
WJ-1110	DN300 Washout at CHJ 155	45	45	22-Dec-14	14-Feb-15	143													
WJ-1020B	Pipe Laying - CHKA 0 - 73 (DN1400) near Realigned TWSR East, 73m long & 4m depth	65	65	11-Jan-15	16-Mar-15	4													
WJ-1100	DN300 Washout at CHJ 212	65	65	12-Jan-15	08-Apr-15	108													
WJ-1020A	Pipe Laying - CHK 0 - 80 (DN1400) near Realigned TWSR East, 80m long & 4m depth	75	75	17-Mar-15	18-Jun-15	4													
<b>Kau Lung Hang Valve Control &amp; Telemetry House Re provision</b>																			
VCTH-1010	BS and E&M Works	90	90	12-Mar-15	03-Jul-15	161													
<b>Stage 1A - Realignment of Tai Wo Service Road West (KD-7)</b>																			
<b>TWSRW Zone 1 between CH100 and CH155</b>																			
<b>At-Grade Roadworks</b>																			
TWSRW-1100	Tree Survey, Tree Felling and Transplanting (All areas at TWSRW)	81	14	16-Oct-13 A	09-Jan-15	-22													
TWSRW-1150	Installation of Cable Ducts for Utilities Diversion Works at Zone 1 & Zone 2 (Approx. 100m) (by utilities undertakers)	167	107	22-Oct-14 A	06-Apr-15	407													
TWSRW-1160	Road Formation, Road Drainage, Kerb, Planter & Pavement	286	255	15-Nov-14 A	06-Nov-15	58													
<b>TWSRW Zone 2 between CH155 and CH280</b>																			
<b>At-Grade Roadworks</b>																			
TWSRW-2120	Road Formation, Road Drainage, Kerb, Planter and Pavement	337	280	16-Oct-14 A	05-Dec-15	33													
<b>TWSRW Zone 3 between CH280 and CH315</b>																			
<b>At-Grade Roadworks</b>																			
TWSRW-3110	Installation of Cable Ducts for Utilities Diversion Works at Zone 3 (Approx. 120m) (by utilities undertakers)	209	209	31-Dec-14*	27-Jul-15	0													
TWSRW-3120	Road Formation, Road Drainage, Kerb, Planter and Pavement	248	248	31-Jan-15	05-Dec-15	33													
<b>TWSRW Zone 4 between CH315 and CH376</b>																			
<b>Construction of Bridge E</b>																			
TWSRW-4000B	CLP Overhead 11KV Cable Diversion at Area B (Phase 2)	140	0	04-Nov-13 A	12-Dec-14 A														
TWSRW-4010A	Pre-Drilling for AE1 (refer to conditions of WSD)	15	1	15-Dec-14 A	22-Dec-14	1372													
TWSRW-4050B	Pile Cap for AE2	50	9	13-Oct-14 A	03-Jan-15	19													
TWSRW-4060	Construction of Temporary Support at DSD nullah (Work in dry season)	45	45	06-Jan-15	05-Mar-15	-27													
TWSRW-4030A	Bored Pile Works for AE1	65	61	17-Dec-14 A	12-Mar-15	3													
TWSRW-4070	In-situ Casting for Bridge Segment (North Bay & Middle Bay)	110	110	06-Mar-15	21-Jul-15	-27													
<b>TWSRW Zone 5 between CH376 and CH520</b>																			
<b>Construction of Retaining Structures</b>																			

Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014		2015				
							Dec	Jan	Feb	Mar	Apr		
TWSRW-5080	Retaining Structure along Slope no. 3SW-C/C898 (to be covered by VO)	45	45	22-Dec-14	14-Feb-15	3							
TWSRW-5090	Lagging Wall Construction and Capping Beam	135	83	06-Nov-14 A	13-Jun-15	3							
<b>At-Grade Roadworks</b>													
TWSRW-5100	Noise Barrier NB2 - Footing and Retaining Structure adjacent to Realigned TWSR West (66m)	90	90	16-Feb-15	13-Jun-15	3							
<b>TWSRW Zone 6 between CH520 and CH530</b>													
<b>Box Culvert Extension - BC01</b>													
TWSRW-6070	Inlet structure of the box culvert BC01 (Covered by VO no. 41)	60	56	17-Dec-14 A	06-Mar-15*	21							
<b>TWSRW Zone 7 between CH530 and CH640</b>													
<b>At-Grade Roadworks</b>													
TWSRW-7130	Road Drainage (incl. Zone 6 & Zone 7)	55	27	03-Nov-14 A	24-Jan-15	6							
TWSRW-7140	Installation of Cable Ducts for Utilities Diversion Works at Area 4 (Approx. 150m) (by utilities undertakers)	251	251	21-Dec-14	28-Aug-15	6							
<b>TWSRW Zone 8 between CH640 and CH695</b>													
<b>Kiu Tau Footbridge Repronisn (West)</b>													
TWSRW-8010	Installation of Socket H-Pile for Proposed Kiu Tau Footbridge (14 nos of Pile)	70	70	10-Jan-15	13-Apr-15	-22							
<b>Remainder of the Works</b>													
TWSRW-9010*	Utilities Diversion in Area 1 (along Re-aligned TWSRW CH100 - CH280)	167	107	22-Oct-14 A	06-Apr-15	407							
TWSRW-9020*	Utilities Diversion in Area 2 (along Re-aligned TWSRW CH 280 - CH315)	209	209	31-Dec-14	27-Jul-15	0							
TWSRW-9040*	Utilities Diversion in Area 4 (along Re-aligned TWSRW CH530 - CH640)	251	251	21-Dec-14	28-Aug-15	6							
<b>Stage N4A &amp; N4B - Realignment of Tai Wo Service Road East (KD-13 &amp; KD-14)</b>													
<b>TWSRE Zone 1 between CH100 and CH270</b>													
<b>At-Grade Roadworks</b>													
TWSRE-1140*	Pipe laying - DN1400 Watermains (CHKA) along Realigned TWSR East	49	49	12-Jan-15	16-Mar-15	4							
<b>TWSRE Zone 2 between CH270 and CH380</b>													
<b>At-Grade Roadworks</b>													
TWSRE-2020	Retaining Wall Construction for FL/RW6	45	15	05-Nov-14 A	10-Jan-15	3							
TWSRE-2030B*	Pipe laying - DN1400 Watermains (CHK) along Realigned TWSR East	75	75	17-Mar-15	18-Jun-15	4							
<b>TWSRE Zone 3 between CH380 and CH456</b>													
<b>At-Grade Roadworks</b>													
TWSRE-3010	Noise Barrier NB3 - Footing adjacent to Realigned TWSR East (62m)	85	85	02-Mar-15	15-Jun-15	33							



- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- Milestone
- Project Baseline Bar

**CEDD Contract No. CV/2012/09**

**Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3**

**3-Month Rolling Programme**

3MPR017








Page 5 of 9

29-Dec-14

3-Month Rolling Programme updated to 2014-12-21

Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014		2015			
							Dec	Jan	Feb	Mar	Apr	
<b>Roundabout A, Slip Road and Access Road</b>												
TWSRE-4000	Site Formation, Preparation Works & Tree Transplant	65	12	15-Apr-14 A	07-Jan-15	118						
TWSRE-4060	Access Road A - Road Formation, Road Drainage, Kerb, Planter and Pavement	134	43	18-Jul-14 A	12-Feb-15	58						
TWSRE-4050B*	Pipe laying - DN2300 Watermains (CHJ) along Access Road A & Roundabout	91	45	20-Jun-14 A	14-Feb-15	13						
TWSRE-4040	Slip Road Y (CH100-CH230) - Road Formation, Road Drainage, Kerb, Planter and Pavement	158	105	18-Sep-14 A	08-May-15	25						
TWSRE-4050A*	Pipe laying - DN600 & DN1200 Watermains (CHB & CHC) along Access Road A & Roundabout	110	110	02-Jan-15	22-May-15	13						
<b>Stage 1C - Viaduct Structure &amp; TCSS Civil Provisions (KD-9)</b>												
<b>Preliminaries</b>												
B-1000A	ADMS Installation inside MTRCL Railway (for pier AD11, AD12, AB10)	14	0	31-Oct-14 A	28-Nov-14 A							
B-1010A	Demonstration to MTRCL (for pier AD11, AD12, AB10)	1	0	29-Nov-14 A	29-Nov-14 A							
B-1020A	Base-line Monitoring (for pier AD11, AD12, AB10)	7	0	29-Nov-14 A	03-Dec-14 A							
B-2030	Completion of CLP Overhead 11KV Cable Diversion at Area B (Phase 2)	0	0		12-Dec-14 A							
B-4030	Erection of Catch Fence at DSD Maintenance Access for AD11	24	0	03-Dec-14 A	20-Dec-14 A							
B-5010	Provide a Temporary Cycle Track (Scheme 2, along DSD maintenance access)	44	44	02-Jan-15	28-Feb-15	33						
B-9000	Trial Operation (AC8 - Early Start on 26 Nov 14)	18	18	02-Mar-15	21-Mar-15	29						
<b>Foundation &amp; Pier Construction</b>												
<b>Bridge A</b>												
BA-16-1000	Pier AA16 - Piling Works	12	0	28-Nov-14 A	11-Dec-14 A							
BA-16-1010	Pier AA16 - Pile Test	7	7	30-Dec-14	07-Jan-15	103						
BA-13-1030	Pier AA13 - Pier Construction	38	30	06-Nov-14 A	28-Jan-15	41						
BA-15-1030	Pier AA15 - Pier Construction	31	31	11-Nov-14 A	29-Jan-15	11						
BA-18-1020	Pier AA18 - Pile Cap	30	30	16-Jan-15	26-Feb-15	124						
BA-14-1030	Pier AA14 - Pier Construction	30	30	17-Jan-15	27-Feb-15	11						
BA-02-1000	Pier AA2W - Piling Works	12	12	02-Mar-15	14-Mar-15	146						
BA-16-1020	Pier AA16 - Pile Cap	30	30	06-Feb-15	19-Mar-15	78						
BA-07-1000	Pier AA7 - Piling Works	24	24	16-Feb-15	21-Mar-15	146						
BA-03-1020	Pier AA3 - Pile Cap	30	30	27-Feb-15	02-Apr-15	124						
BA-01-1000	Abutment AA1 - Piling Works	24	24	16-Mar-15	16-Apr-15	256						
BA-02-1020A	Pier AA2E - Pile Cap	30	30	20-Mar-15	28-Apr-15	109						

 <b>俊和建築工程有限公司</b> CHUN WO CONSTRUCTION & ENGINEERING CO., LTD.	 Actual Work  Remaining Work  Summary Bar  Critical Remaining Work  Milestone  Project Baseline Bar	<b>CEDD Contract No. CV/2012/09</b>  <b>Liantang / Heung Yuen Wai BCP - Site Formation &amp; Infrastructure Works, Contract 3</b>  <b>3-Month Rolling Programme</b>	3-Month Rolling Programme updated to 2014-12-21 <table border="1"> <thead> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approved</th> </tr> </thead> <tbody> <tr> <td>29-Dec-14</td> <td>Rev.1</td> <td>SL</td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>	Date	Revision	Checked	Approved	29-Dec-14	Rev.1	SL													
	Date	Revision	Checked	Approved																			
	29-Dec-14	Rev.1	SL																				
		<b>3MPR017</b>	<b>Page 6 of 9</b>																				
			<b>29-Dec-14</b>																				

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014				2015				
							Dec	Jan	Feb	Mar	Apr				
<b>Bridge B</b>															
BB-08-1020B	Pier AB8W - Pile Cap	30	0	04-Nov-14 A	22-Nov-14 A					Pier AB8W - Pile Cap					
BB-09-1000	Pier AB9 - Piling Works	24	0	25-Oct-14 A	22-Nov-14 A					Pier AB9 - Piling Works					
BB-08-1020A	Pier AB8E - Pile Cap	30	0	03-Nov-14 A	29-Nov-14 A						Pier AB8E - Pile Cap				
BB-07-1010	Pier AB7 - Pile Test	7	7	13-Sep-14 A	31-Dec-14	-71				Pier AB7 - Pile Test, Pier AB7 - Pile Test					
BB-09-1010	Pier AB9 - Pile Test	7	7	01-Dec-14 A	31-Dec-14	16				Pier AB9 - Pile Test, Pier AB9 - Pile Test					
BB-06-1020B	Pier AB6W - Pile Cap	30	7	26-Nov-14 A	31-Dec-14	228					Pier AB6W - Pile Cap, Pier AB6W - Pile Cap				
BB-10-1000	Pier AB10 - Piling Works	24	9	04-Dec-14 A	03-Jan-15	-1				Pier AB10 - Piling Works, Pier AB10 - Piling Works					
BB-08-1040	Pier AB8E - Pier Construction	24	24	22-Dec-14	21-Jan-15	-88				Pier AB8E - Pier Construction					
BB-08-1030	Pier AB8W - Pier Construction	24	24	29-Dec-14*	26-Jan-15	-62				Pier AB8W - Pier Construction					
BB-10-1010	Pier AB10 - Pile Test	7	7	21-Jan-15	28-Jan-15	-1				Pier AB10 - Pile Test					
BB-07-1020	Pier AB7 - Pile Cap	30	30	02-Jan-15	05-Feb-15	-71					Pier AB7 - Pile Cap				
BB-09-1020	Pier AB9 - Pile Cap	30	30	19-Jan-15	28-Feb-15	2					Pier AB9 - Pile Cap				
BB-11-1000	Pier AB11 - Piling Works	24	24	02-Feb-15	07-Mar-15	43					Pier AB11 - Piling Works				
BB-07-1030	Pier AB7 - Pier Construction	24	24	06-Feb-15*	12-Mar-15	-71					Pier AB7 - Pier Construction				
BB-10-1020	Pier AB10 - Pile Cap	30	30	06-Feb-15	19-Mar-15	-8					Pier AB10 - Pile Cap				
BB-08-1050	Portal AB8 - Portal Construction	45	45	22-Jan-15	21-Mar-15	-88					Portal AB8 - Portal Construction				
BB-09-1030	Pier AB9 - Pier Construction	24	24	13-Mar-15	14-Apr-15	-8									
<b>Bridge C</b>															
BC-05-1020	Pier AC5 - Pile Cap	30	0	06-Oct-14 A	27-Nov-14 A					Pier AC5 - Pile Cap					
BC-12-1000	Pier AC12 - Piling Works	12	0	12-Nov-14 A	29-Nov-14 A					Pier AC12 - Piling Works					
BC-09-1020	Pier AC9 - Pile Cap	30	0	05-Nov-14 A	12-Dec-14 A					Pier AC9 - Pile Cap					
BC-08-1030	Pier AC8 - Pier Construction	24	2	13-Sep-14 A	23-Dec-14	29				Pier AC8 - Pier Construction, Pier AC8 - Pier Construction					
BC-12-1010	Pier AC12 - Pile Test	7	7	08-Dec-14 A	31-Dec-14	-71				Pier AC12 - Pile Test, Pier AC12 - Pile Test					
BC-11-1020	Pier AC11 - Pile Cap	30	9	24-Nov-14 A	03-Jan-15	186					Pier AC11 - Pile Cap, Pier AC11 - Pile Cap				
BC-06-1030	Pier AC6 - Pier Construction	24	16	21-Oct-14 A	12-Jan-15	78				Pier AC6 - Pier Construction, Pier AC6 - Pier Construction					
BC-07-1030	Pier AC7 - Pier Construction	24	20	10-Nov-14 A	16-Jan-15	11				Pier AC7 - Pier Construction, Pier AC7 - Pier Construction					
BC-10-1020	Pier AC10 - Pile Cap	30	21	23-Dec-14 A	17-Jan-15	2					Pier AC10 - Pile Cap				
BC-12-1020	Pier AC12 - Pile Cap	30	30	02-Jan-15	05-Feb-15	-71					Pier AC12 - Pile Cap				



- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- Milestone
- Project Baseline Bar

**CEDD Contract No. CV/2012/09**

**Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3**

**3-Month Rolling Programme**

3MPR017


Page 7 of 9

29-Dec-14

3-Month Rolling Programme updated to 2014-12-21

Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	



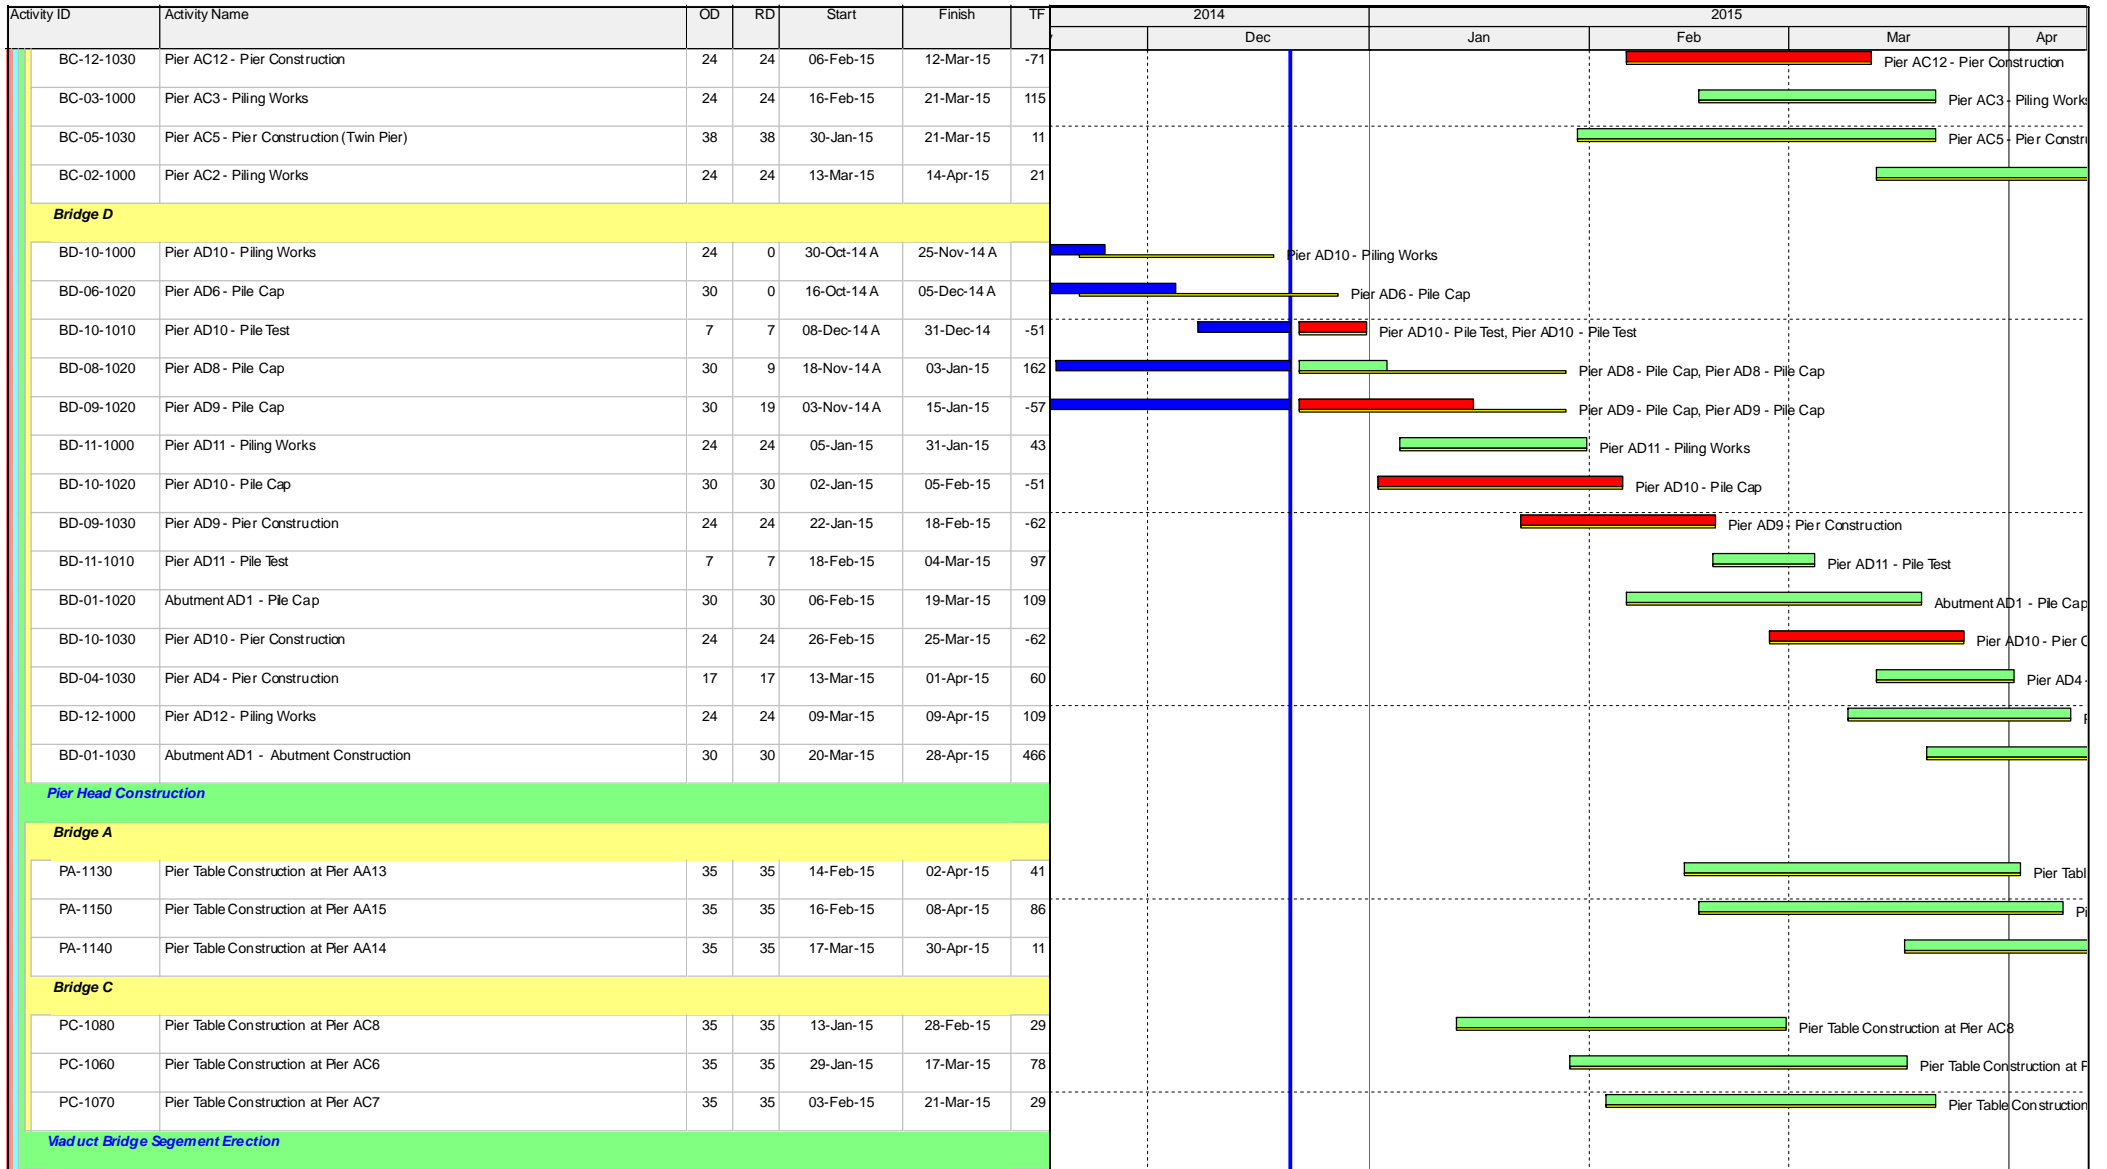







- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- Milestone
- Project Baseline Bar

Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2014		2015				
							Dec	Jan	Feb	Mar	Apr		
<b>Bridge C</b>													
EC-1080	Bridge Deck Construction at Pier AC8 by Typical Lifting Frame (24 nos)	18	18	02-Mar-15	21-Mar-15	29						Bridge Deck Construct	
<b>Section VI - Works in Portion FH9 (KD-6A)</b>													
<b>Preliminary Preparation Works</b>													
S6-1000	Completion of Temporary Vehicular Bridge by C2 Contractor	0	0		31-Dec-14	55						◆ Completion of Temporary Vehicular Bridge by C2 Contractor	
S6-1020	Site Clearance and Site Formation	14	14	02-Jan-15	17-Jan-15	55						Site Clearance and Site Formation	

-  Actual Work
-  Remaining Work
-  Summary Bar
-  Critical Remaining Work
-  Milestone
-  Project Baseline Bar

Date	Revision	Checked	Approved
29-Dec-14	Rev.1	SL	
