





## Appendix A Construction Programme


Activity ID	Activity Name	OD	RD	Start	Finish	2018							
						Feb	Mar		, , , , , , , , , , , , , , , , , , ,	Apr	Ma	ay	Jun
Updated Mas	ter Programme (UMP05E)												
Key Dates (Co	ontractual)												
KD-0400	KD4: Section 3 - Remainder of Landscape Softworks not included in Section 3A	0	0		30-Jan-18 A	D4: Section 3 - Remainder of Landscape Softw	orks not included in Section 3A						
KD-0100a	KD1: Section 1A - all HyD's works in Zone3 & SBZ2 excl. Landscape Works (Contractural)	0	0		05-Feb-18 A	♦ KD1: Section 1A - all HyD's works in:	Zone 3 & SBZ2 excl. Landscape	Works (Contractura	al)				
KD-0300b	KD3: Section 2 - the remainder of the Works (Contractual)	0	0		05-Feb-18 A	♠ KD3: Section 2 - the remainder of the	Works (Contractual)						
KD-1200a	KD9: Stage 1C - Completion of viaduct structures & civil provisions for TCSS (Preli. EOT by Claim 56 & 58)	0	0		09-Feb-18 A	♦ KD9: Stage 1C - Completion o	viaduct structures & civil provis	ions for TCSS (Prel	i. EOT by Claim 56 & 58)				
Key Dates (Fo													
KD-1205	KD9: Stage 1C - Completion of viaduct structures and associated civil provisions for TCSS	0	0		09-Feb-18 A	♦ KD9: Stage 1C - Completion of	viaduct structures and associate	d civil provisions fo	r TCSS				
Tentative Han	dover Schedule to TCSS contractor												
HS-D2	Allow access for TCSS contractor to carry out TCSS installation works on Bridge D (from AD 10 to AD 14)	0	0		09-Feb-18 A	♠ Allow access for TCSS contract	tor to carry out TCSS installation	nworks on Bridge [	(from AD10 to AD14)				
Dependent Mi	lestones from Other Contracts												
Related to No	orth Buffer Zone												
MS-NBZ150	Shift existing FLH SB Middle Lane to future FLH 2nd Lane by FHW3 Contractor (NBZ)	0	0	10-Feb-18 A		◆ Shift existing FLH SB Middle I	ane to future FLH 2nd Lane by	FHW3 Contractor (	(NBZ)				
MS-NBZ110	, , , , , , , , , , , , , , , , , , ,	0	0	28-Apr-18*						<b>♦</b> S	Shift existing FLH NB Slow L	ane to future hard sh	oulder by FHW3
MS-NBZ120	Shift existing FLH NB Middle Lane to future 1st Lane by FHW3 Contractor (NBZ)	0	0	26-May-18*								♦ Sh	ift existing FLH I
Major Milesto	nes and Events												
MS-0320a	Diversion on re-aligned TWSRE (1 way Traffic)	0	0	30-Jan-18 A		iversion on re-aligned TWSRE (1 way Traffic)							
MS-0320b	Commissioning of re-aligned TWSRE (2 ways Traffic)	0	0	24-Apr-18*						◆ Commis	ssioning of re-aligned TWSF	RE (2 ways Traffic)	
MS-1060d	T6d: TTA to shift FLH SB eastward (shift 3 Lanes) (South Portion)	1	1	07-May-18*	07-May-18						■ T6d: TTA to sl	hift FLH SB eastward	(shift 3 Lanes) (S
MS-0330	Watermains Connection for Contract 2 (Viaduct)	0	0		28-May-18							•	Watermains Co
Design and S	ubmissions												
Design Confi	rmation												
PRE-1620	Procument and Deleivery (3 mth) of LED Street Lighting	68	37	16-Jan-18 A	07-May-18						Procument a	and Deleivery (3 mth)	of LED Street Lig
Method State	ment and Design (Major) Approved by AECOM												
PRE-2040	E&M design for lighting inside void of viaduct (redesign for lux design change, VO to be provided)	60	0	01-Apr-16 A	26-Feb-18 A	E&	M design for lighting inside void	of viaduct (redesigr	for lux design change, V	O to be provided)			
PRE-2030	E&M design for Public Llighting of Kiu Tau Footbridge (further comments provided by HyD/Lightings)	60	41	05-Sep-16 A	11-May-18							design for Public Lligi	
Section IA & I	B - Fanling Highway Widening (KD-1 & KD-2)												
Fanling High	way South Portion between CH6935 and CH7470												
Fanling High	hway Zone 1 between CH6935 and CH7130 (within SBZ2)												
Noise Barri	er												
FHW-1140	Noise Barrier NB70 - Footing adjacent to SB lane (Bay 1 - 3)	42	61	19-Dec-17 A	05-Jun-18						<u> </u>		N
FHW-1140	b Watermain DN600 Diversion (suit for permanent purpose and VO199 for extension	61	61	20-Mar-18*	05-Jun-18								w
	of NB70) oadworks (195m)												
											<u>i</u>		
			Actua	ıl Work		CEDD Con	tract No. CV/20	12/09		3-Month R	Rolling Programme up	pdated to 2018-	3-20
			Rema	aining Work					tion &	Date	Revision	Checked	Approved
	Summary Bar				Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3								
	俊和建築工程有限公司 Critical Remaining Work				3-Month Rolling Programme								
Сн	UN WO CONSTRUCTION & ENGINEERING CO., LTD.	•	Milest	_						<del></del>		+	
				ct Baseline B	ar	UMP05E	Page 1 of 9	20	-Mar-18	<del>                                     </del>			
			-,-						ľ				
					1								

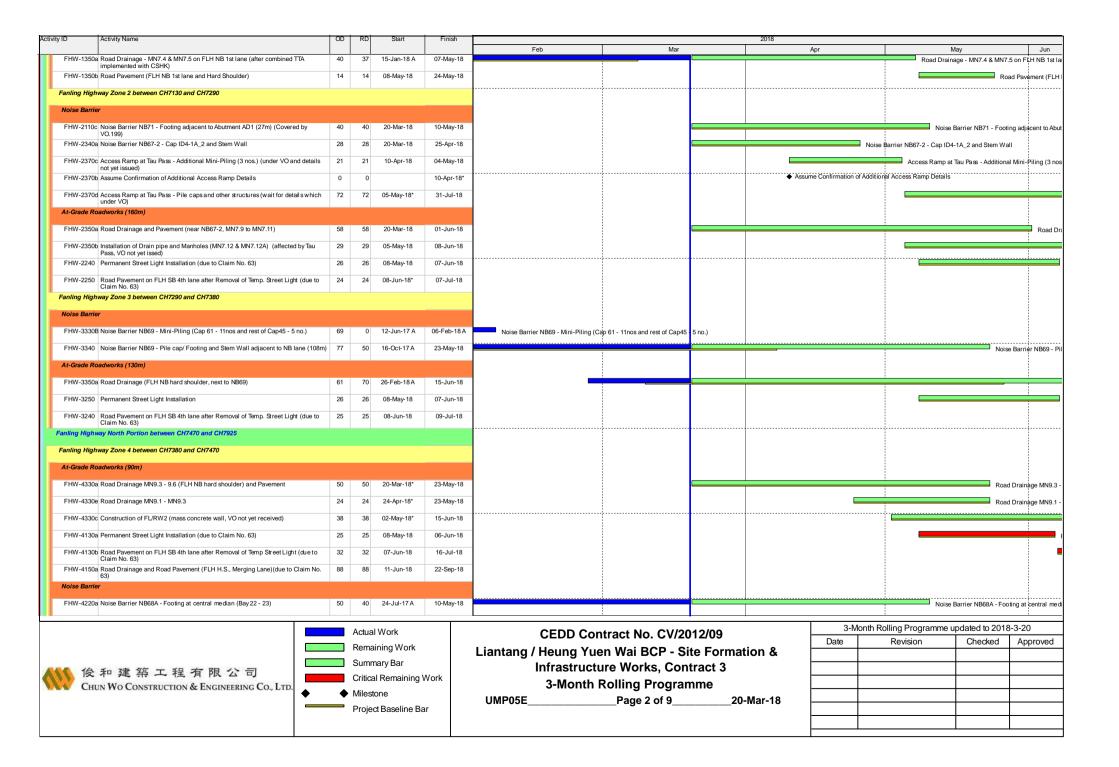


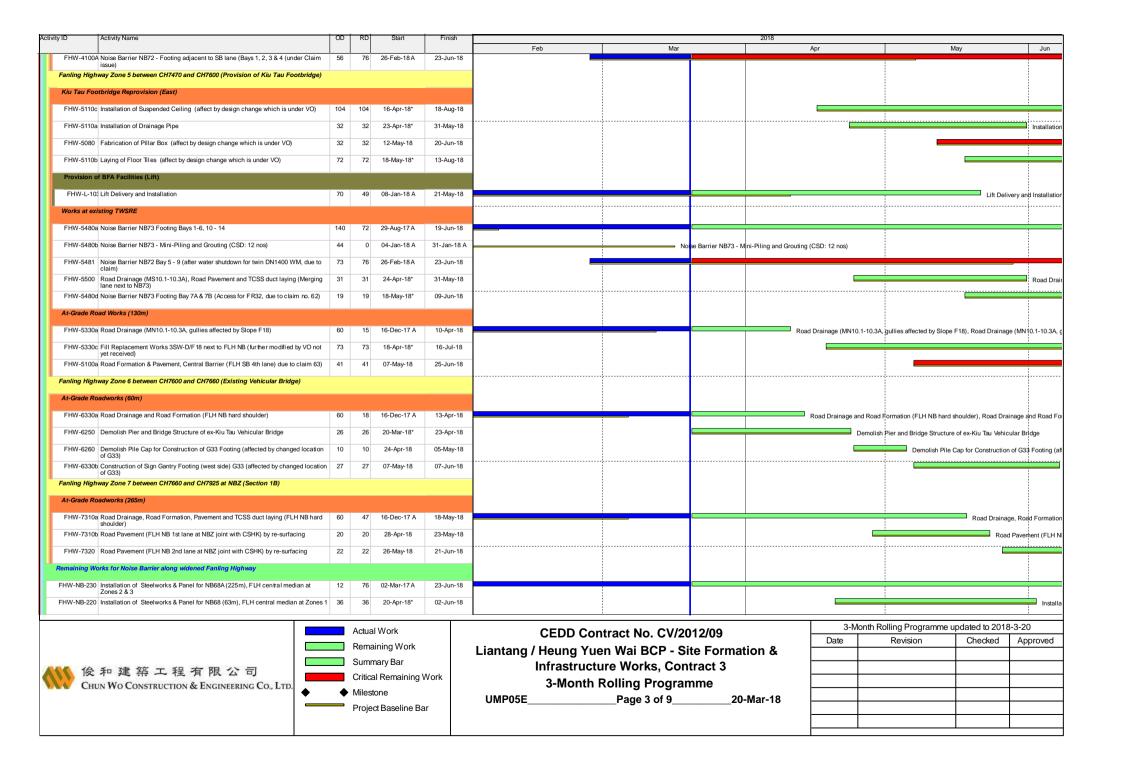


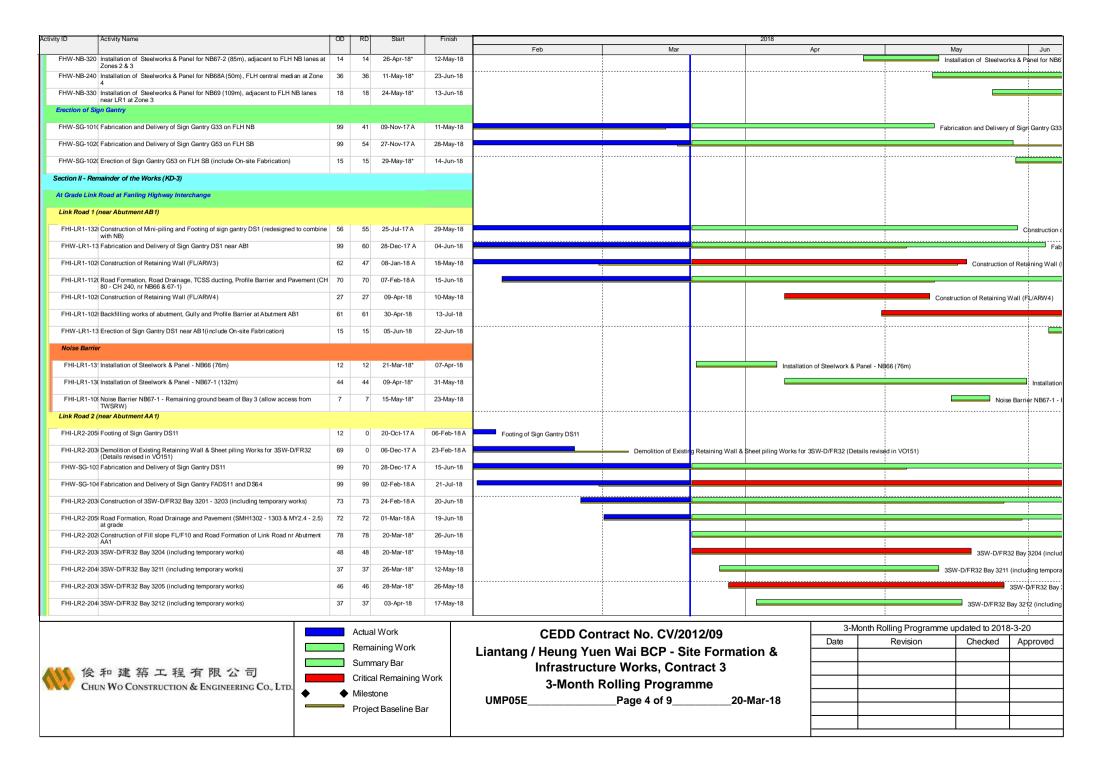

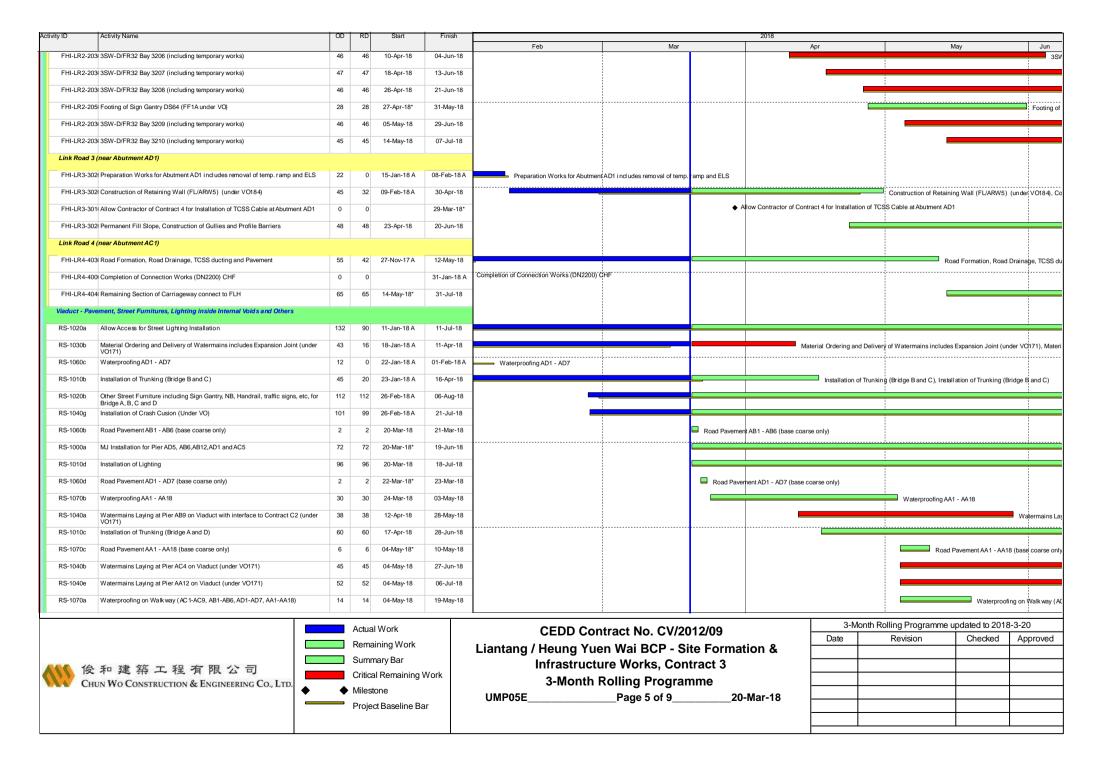

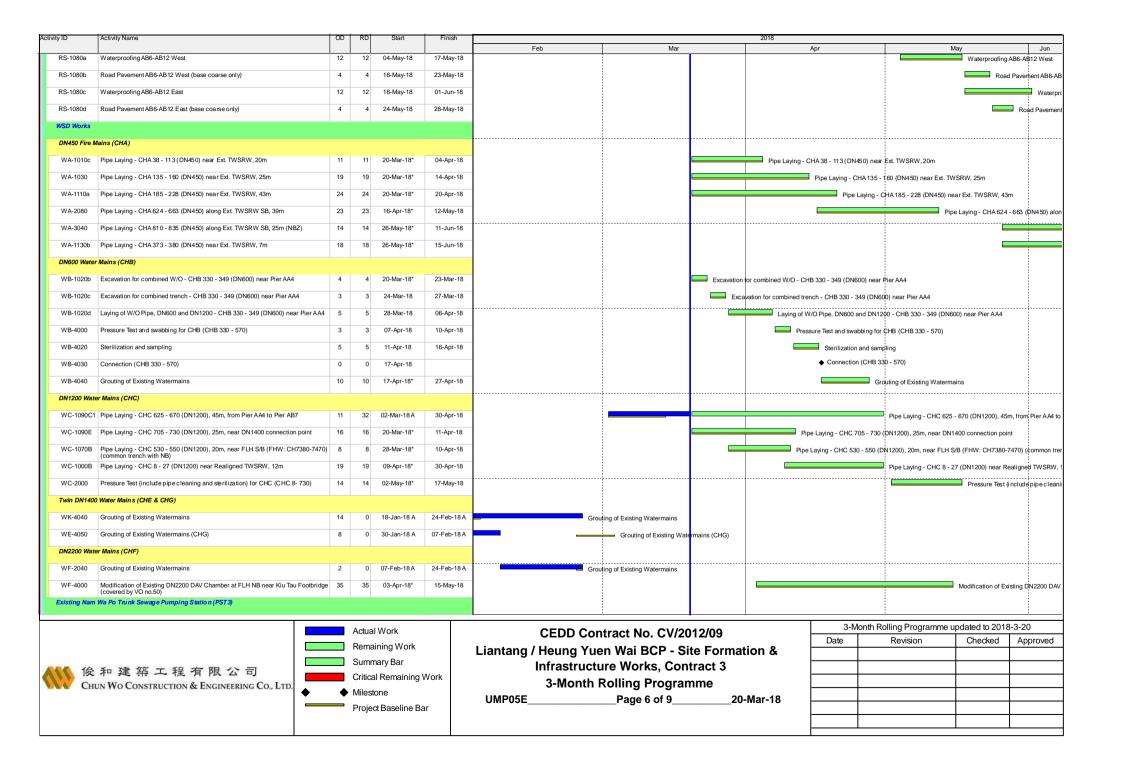

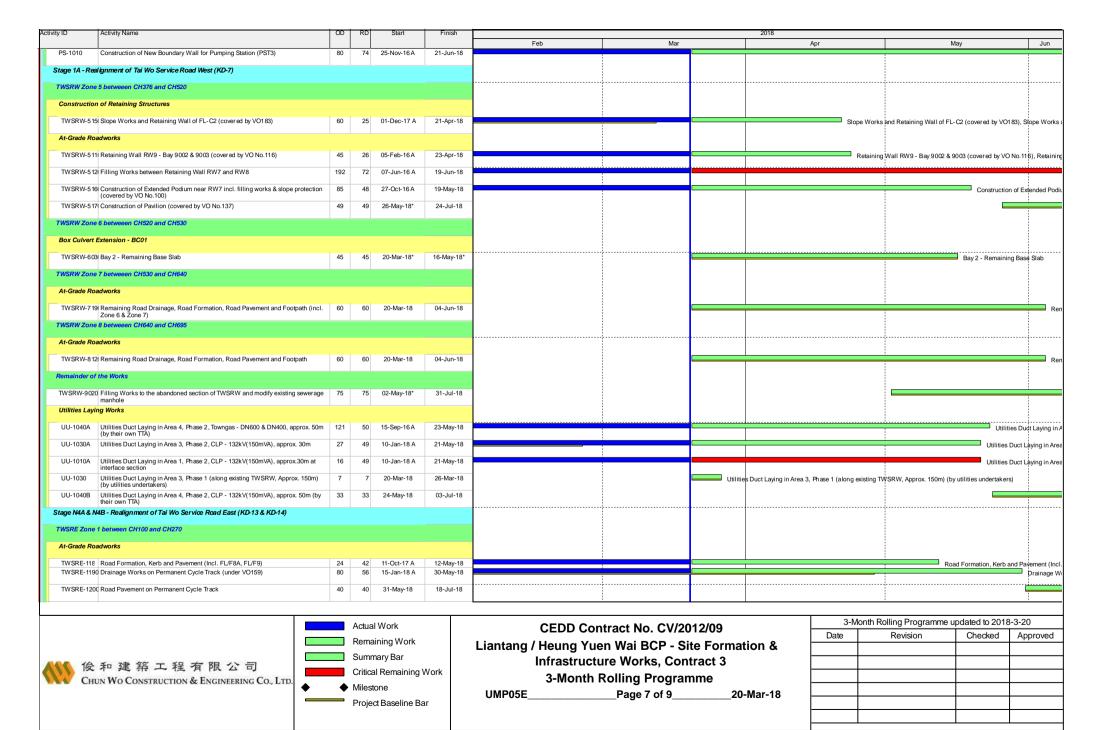

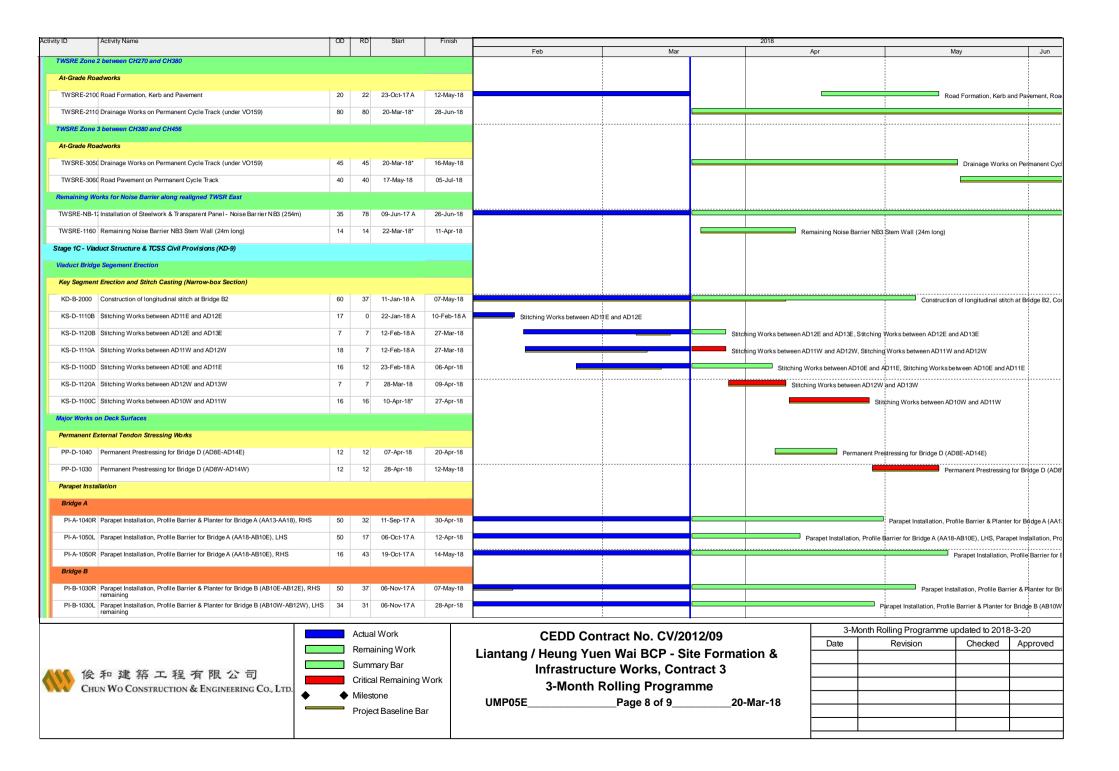

ctivity ID Activity Name			RD	Start	Finish	2018					
						Feb	Mar		Apr	May	Jun
Bridge C											
PI-C-1040	R Parapet Installation, Profile Barrier for Bridge C (AC11-AD10E), RHS	63	63	20-Mar-18	07-Jun-18		]			:	<del></del>
Bridge D											
PI-D-1020	R Parapet Installation, Profile Barrier & Planter for Bridge D (AD5-AD8W), RHS	78	54	09-May-17 A	28-May-18					Pa	Parapet Inst
PI-D-1020	Parapet Installation, Profile Barrier for Bridge D (AD5-AD8W), LHS	90	54	11-May-17 A	28-May-18					Pa	Parapet Ins
PI-D-1010	R Parapet Installation, Profile Barrier & Planter for Bridge D (AD1-AD5), RHS	83	30	16-Jun-17 A	27-Apr-18				Pai	apet Installation, Profile Barrier & Planter for Bridge	je D (AD1
PI-D-1010	Parapet Installation, Profile Barrier & Planter for Bridge D (AD1-AD5), LHS	52	26	03-Jul-17 A	23-Apr-18					stallation, Profile Barrier & Planter for Bridge D (Al	
PI-D-1040	TC TCSS duct laying and Provision of Access for TCSS Contractor - Bridge D	12	0	18-Jan-18 A	09-Feb-18 A	TCSS duct laying and Provision of Access for	TCSS Contractor	Bridge D			
PI-D-1030	Parapet Installation, Profile Barrier for Bridge D (AD8W-AD10W), LHS	39	39	21-Apr-18	07-Jun-18						$\dot{+}$
PI-D-1040	RI Parapet Installation for Bridge D (AD10E-AD14E), RHS	48	48	21-Apr-18	19-Jun-18						$\dot{+}$
PI-D-1040	LN Parapet Installation for Bridge D (AD10W-AD14W), LHS	30	30	14-May-18	19-Jun-18						<del>-</del>
Landscaping	& Establishment Works (KD-4, 4A, 5, 5A, 6)										
Secton 3 - R	emainder of Landscaping Softworks Not Included in Secton 3A										
S3-1000	Transplant and Landscaping Softworks on At grade Road	131	131	26-Mar-18*	03-Sep-18						4
S3-1010	Transplant and Landscaping Softworks on Vlaductor other remaining area	69	69	16-May-18*	07-Aug-18						$ \leftarrow $





3-Month Rolling Programme updated to 2018-3-20										
Date	Revision	Checked	Approved							
·										
