






Appendix A Construction Programme

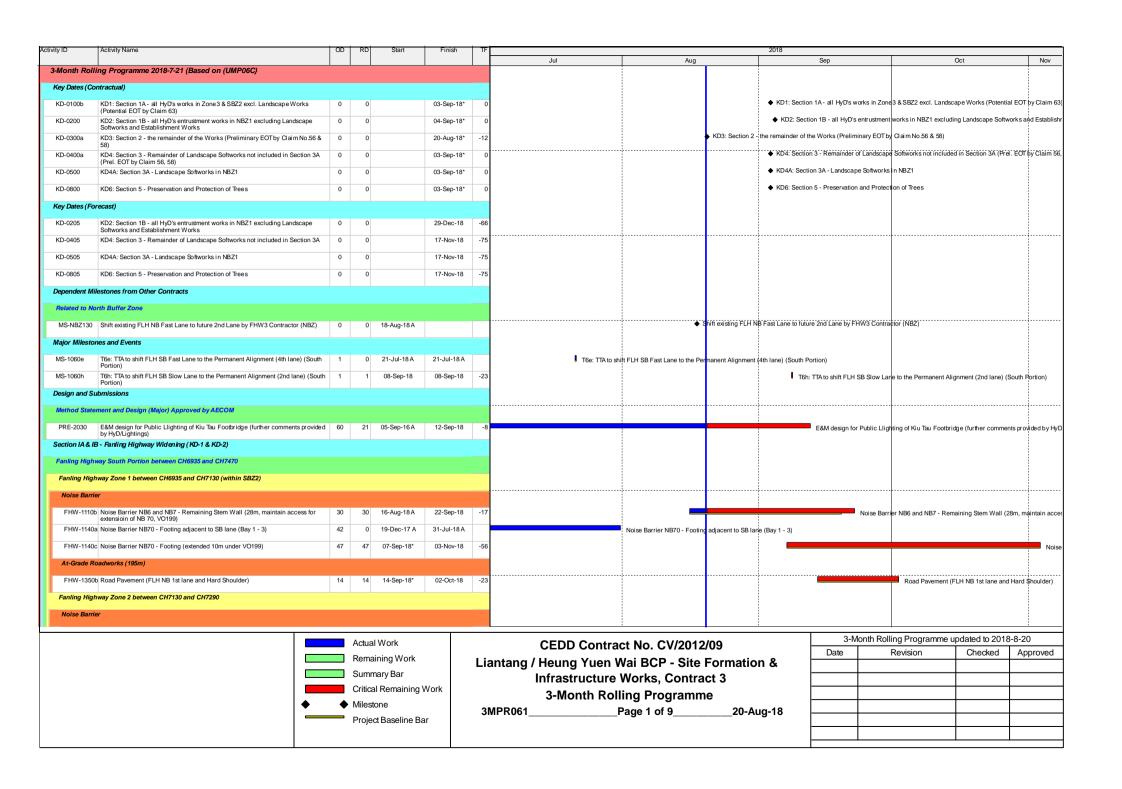


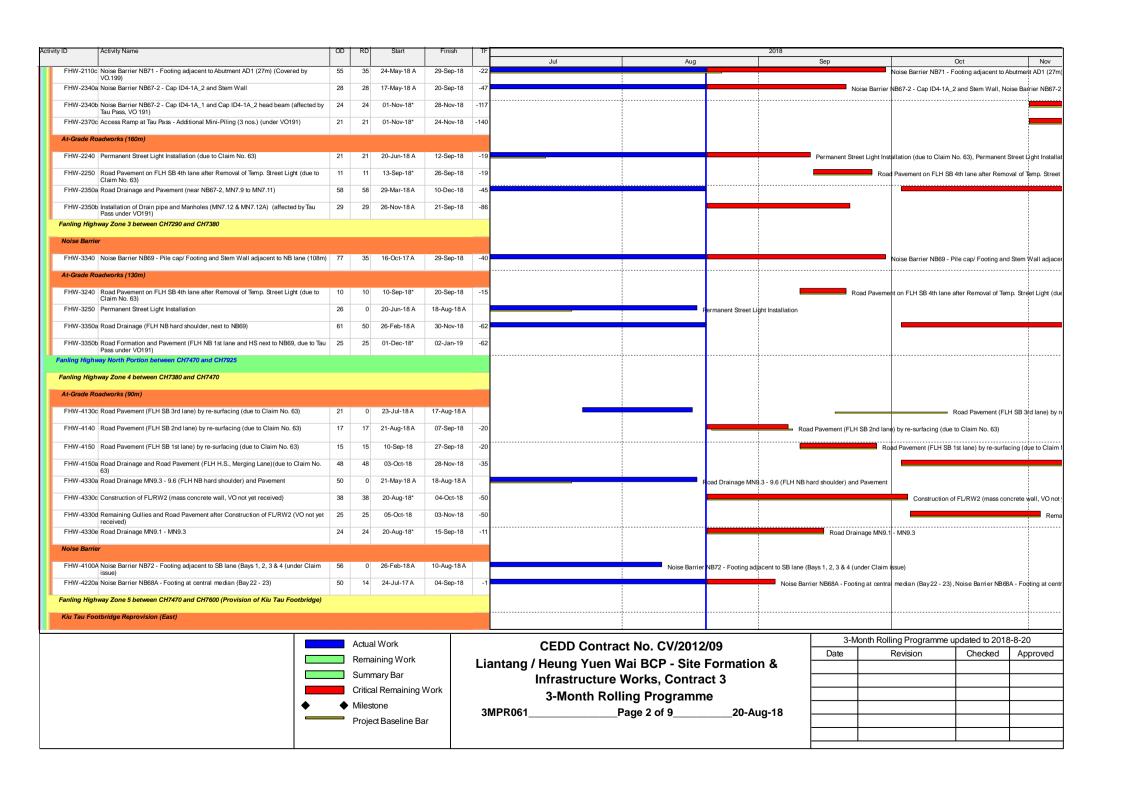


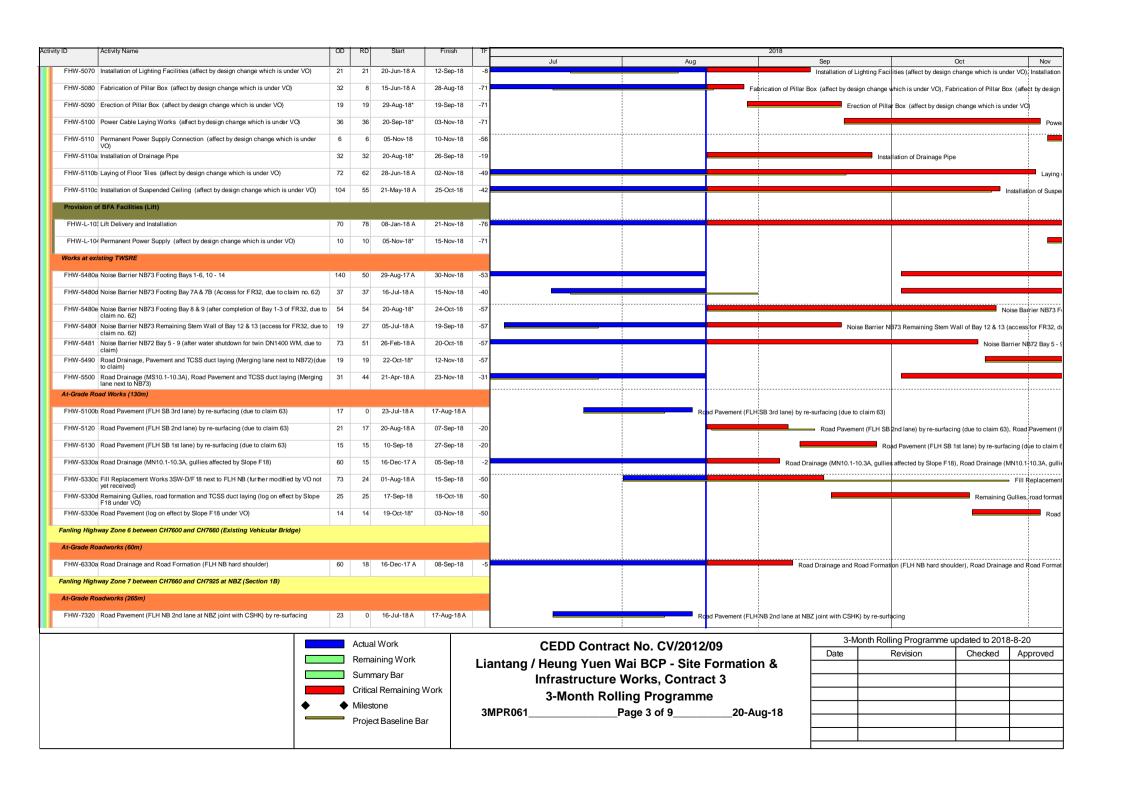


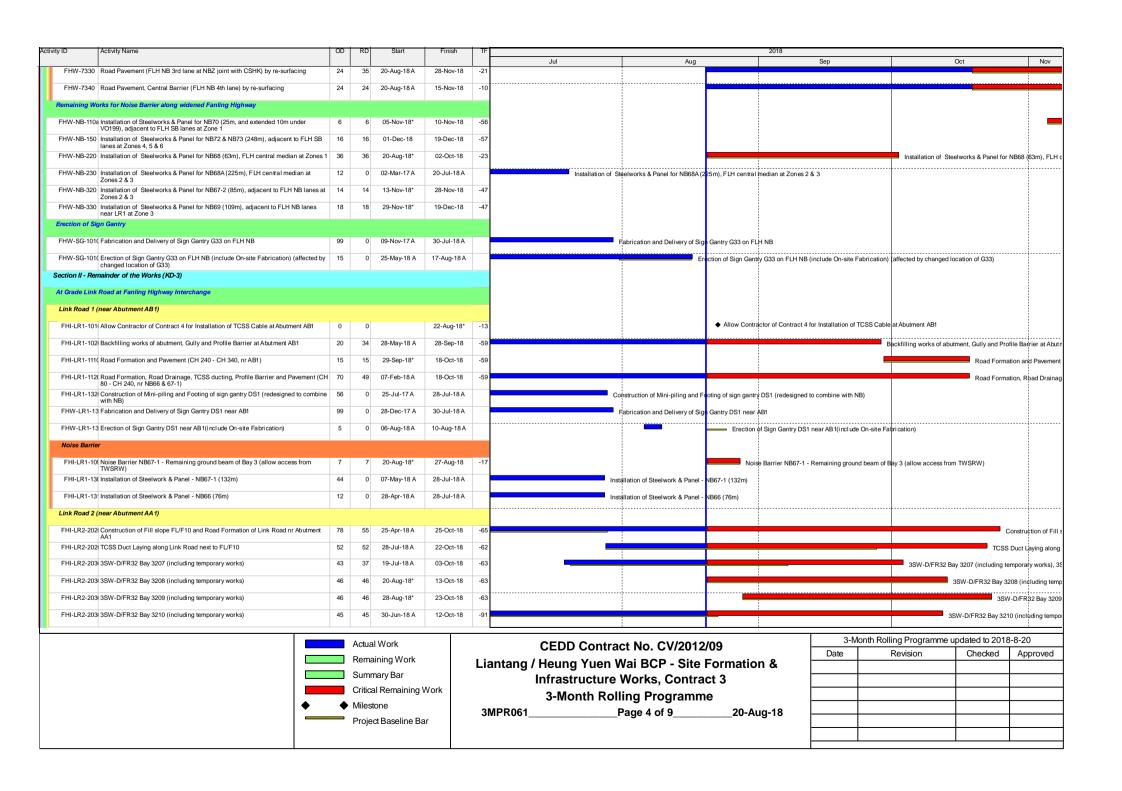

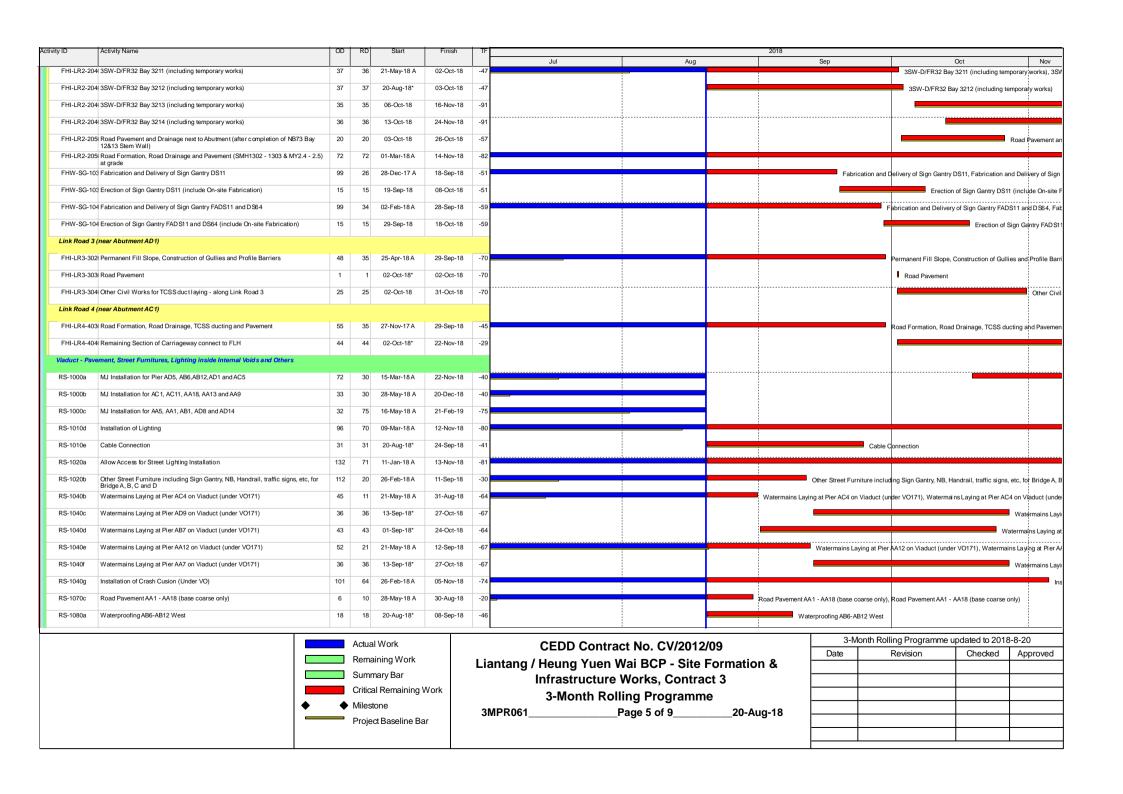


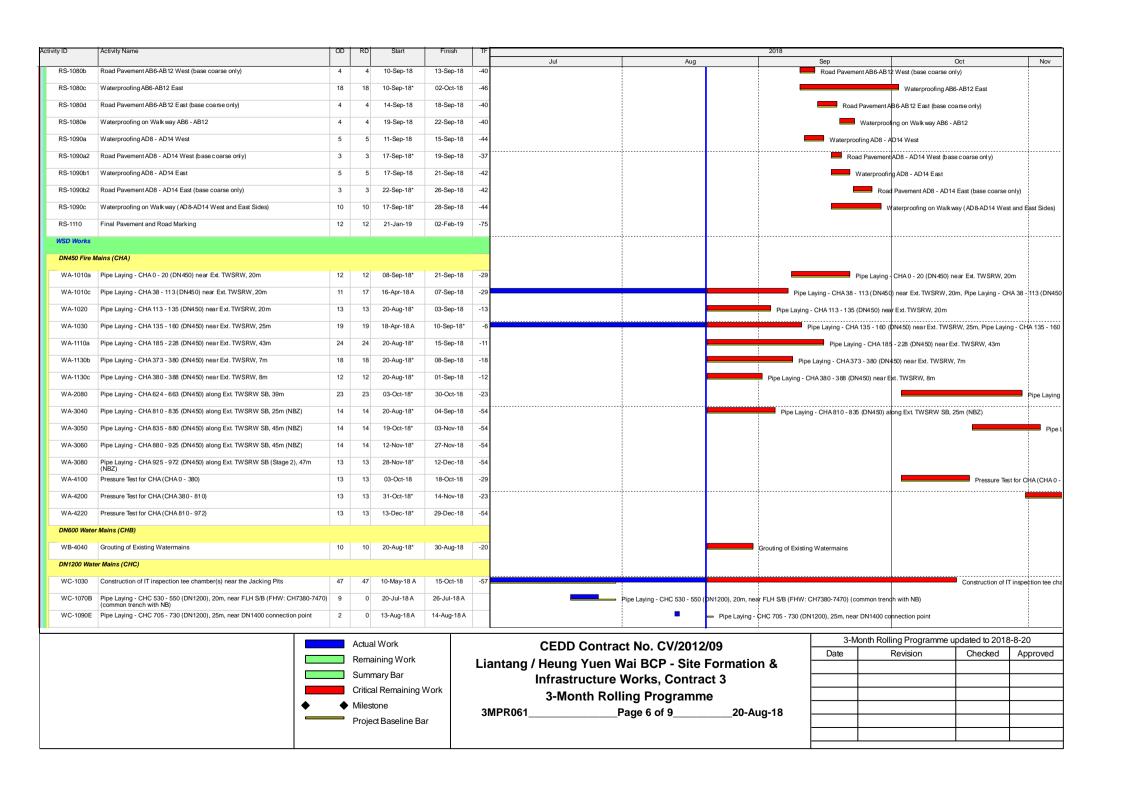

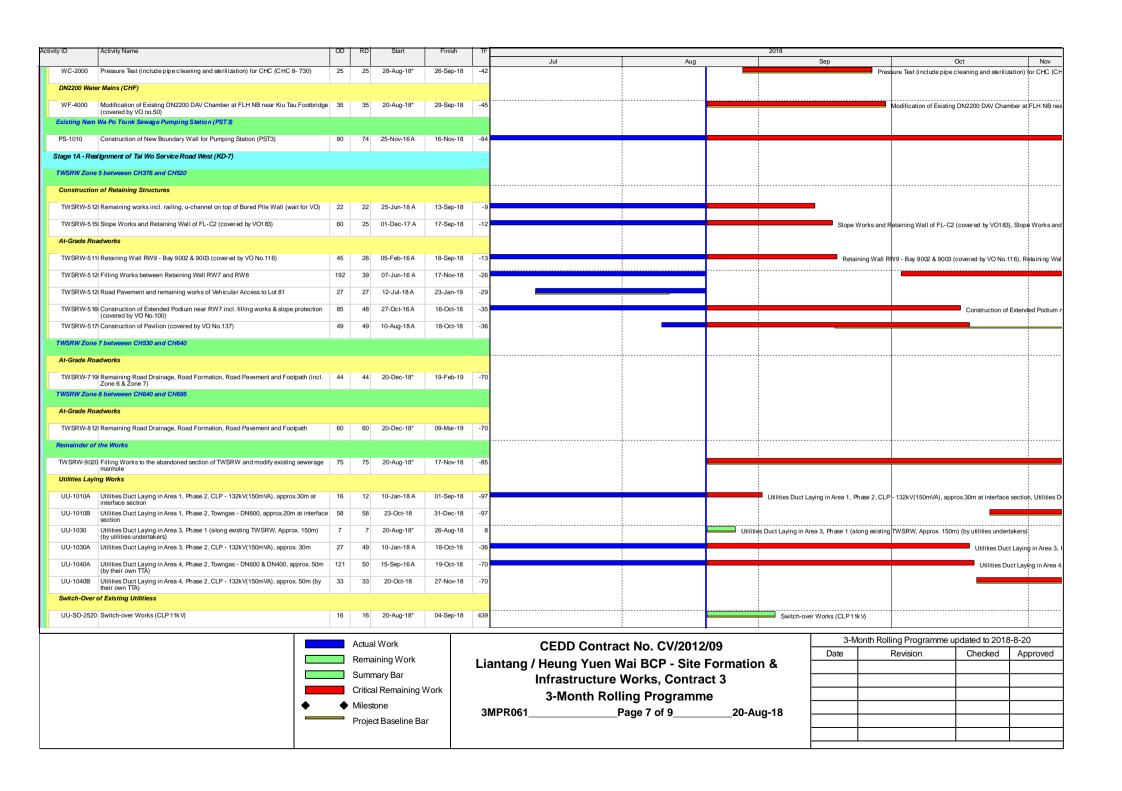

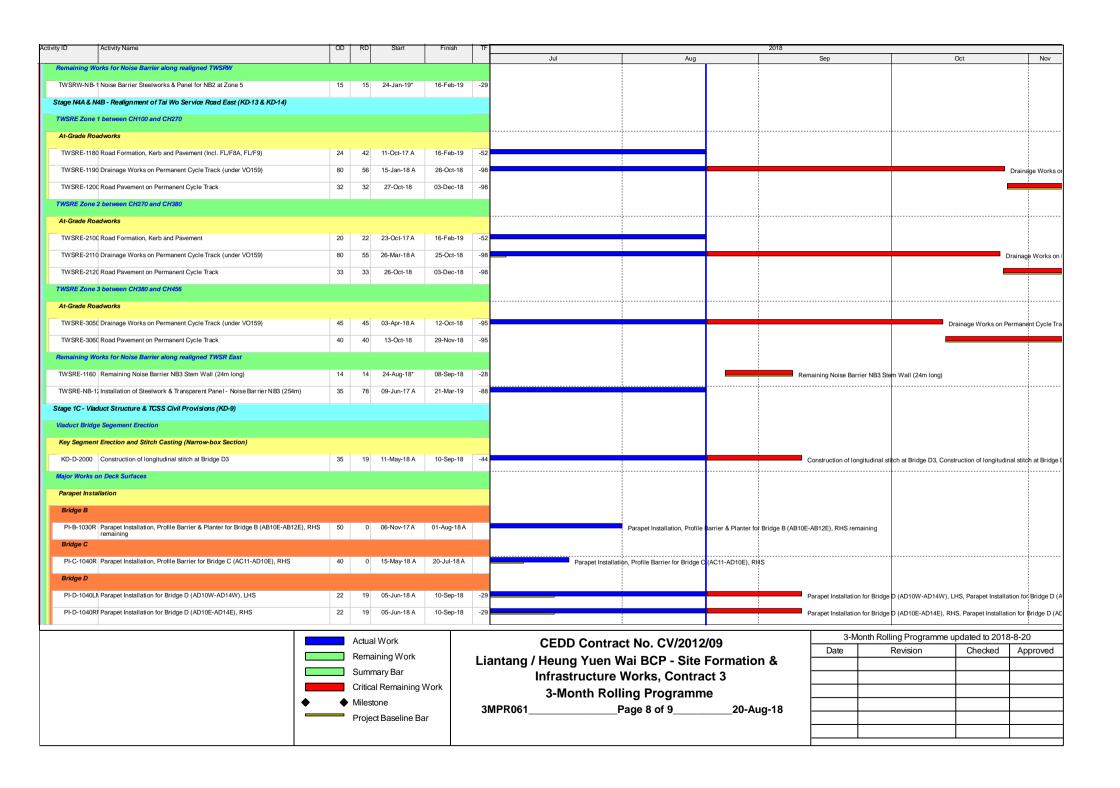

tivity ID	Activity Name	OD	RD	Start	Finish	TF	2018					
							Jul	Aug		Sep	Oct	N
Landscaping	& Establishment Works (KD-4, 4A, 5, 5A, 6)	<u>'</u>										
Secton 3A -	Landscaping Softworks in NBZ1											
S3A-1000	Transplant and Landscaping Softworks in NBZ1	50	50	20-Aug-18*	19-Oct-18	-38		-			Transp	lant and Landsca
Secton 3 - R	emainder of Landscaping Softworks Not Included in Secton 3A											
S3-1000	Transplant and Landscaping Softworks on At grade Road	131	75	26-Mar-18 A	17-Nov-18	-62						
S3-1010	Transplant and Landscaping Softworks on Vlaductor other remaining area	48	48	20-Aug-18*	16-Oct-18	-35		<u>-</u>			Transplant a	and Landscaping
							:					i
Section 4A:	Establishment Works for Landscape Softworks under Section 3A											
Section 4A: S4A-1000	Establishment Works for Landscape Softworks under Section 3A Establishment Works at NBZ1	365	365	20-Oct-18	19-Oct-19	-48						
S4A-1000		365	365	20-Oct-18	19-Oct-19	-48						
S4A-1000	Establishment Works at NBZ1	365	365		19-Oct-19	-48						
\$4A-1000 Section 4: E \$4-1000	Establishment Works at NBZ1 stablishment Works for Landscape Softworks under Section 3											



3-Month Rolling Programme updated to 2018-8-20									
Date	Revision	Checked	Approved						
