

Appendix A Construction Programme

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2019					
							Mar	Apr	May	Jun	Jul	Aug
3-Month Rolling Programme 2019-4-21 (Based on UMP06C)												
Key Dates (Contractual)												
KD-0400a	KD4: Section 3 - Remainder of Landscape Softworks not included in Section 3A (Pref. EOT by Claim 56, 58)	0	0		20-May-19*	0						◆ KD4: Section 3 - Remainder of Landscape Softworks not included in Section 3A (Pref. EOT by Claim 56, 58)
KD-0500	KD4A: Section 3A - Landscape Softworks in NBZ1 (Potential EOT by Inclement Weather)	0	0		20-May-19*	-213						◆ KD4A: Section 3A - Landscape Softworks in NBZ1 (Potential EOT by Inclement Weather)
KD-0800	KD6: Section 5 - Preservation and Protection of Trees (Potential EOT by Inclement Weather)	0	0		20-May-19*	-110						◆ KD6: Section 5 - Preservation and Protection of Trees (Potential EOT by Inclement Weather)
Key Dates (Forecast)												
KD-0405	KD4: Section 3 - Remainder of Landscape Softworks not included in Section 3A	0	0		20-May-19	1						◆ KD4: Section 3 - Remainder of Landscape Softworks not included in Section 3A
KD-0505	KD4A: Section 3A - Landscape Softworks in NBZ1	0	0		20-May-19	-213						◆ KD4A: Section 3A - Landscape Softworks in NBZ1
KD-0805	KD6: Section 5 - Preservation and Protection of Trees	0	0		20-May-19	-110						◆ KD6: Section 5 - Preservation and Protection of Trees
Section IA & IB - Fanling Highway Widening (KD-1 & KD-2)												
Fanling Highway South Portion between CH6935 and CH7470												
Fanling Highway Zone 1 between CH6935 and CH7130 (within SBZ2)												
Noise Barrier												
FHW-1110b	Noise Barrier NB6 and NB7 - Remaining Stem Wall (28m, maintain access for extension of NB 70, VO199)	30	0	16-Aug-18 A	30-Apr-19 A		Noise Barrier NB6 and NB7 - Remaining Stem Wall (28m, maintain access for extension of NB 70, VO199)					
FHW-1140c	Noise Barrier NB70 - Footing (extended 10m under VO199)	153	0	20-Feb-19 A	30-Apr-19 A		Noise Barrier NB70 - Footing (extended 10m under VO199)					
At-Grade Roadworks (195m)												
FHW-1350b	Road Pavement (FLH NB 1st lane and Hard Shoulder)	138	0	20-Mar-19 A	20-May-19 A		Road Pavement (FLH NB 1st lane and Hard Shoulder)					
Fanling Highway Zone 2 between CH7130 and CH7290												
Noise Barrier												
FHW-2340b	Noise Barrier NB67-2 - Cap ID4-1A_1 and Cap ID4-1A_2 head beam (affected by Tau Pass, VO 191)	15	0	23-Apr-19 A	10-May-19 A		Noise Barrier NB67-2 - Cap ID4-1A_1 and Cap ID4-1A_2 head beam (affected by Tau Pass, VO 191)					
FHW-2370c	Access Ramp at Tau Pass - Additional Mini-Piling (3 nos.) (under VO191)	34	0	20-Feb-19 A	28-Apr-19 A		Access Ramp at Tau Pass - Additional Mini-Piling (3 nos.) (under VO191)					
FHW-2370d	Access Ramp at Tau Pass - Pile caps and other structures (under VO191)	48	0	07-Mar-19 A	03-May-19 A		Access Ramp at Tau Pass - Pile caps and other structures (under VO191)					
At-Grade Roadworks (160m)												
FHW-2240	Permanent Street Light Installation (due to Claim No. 63)	21	0	20-Jun-18 A	13-Mar-19 A		Permanent Street Light Installation (due to Claim No. 63)					
FHW-2250	Road Pavement on FLH SB 4th lane after Removal of Temp. Street Light (due to Claim No. 63)	11	0	20-Mar-19 A	10-Apr-19 A		Road Pavement on FLH SB 4th lane after Removal of Temp. Street Light (due to Claim No. 63)					
FHW-2350a	Road Drainage and Pavement (near NB67-2, MN7.9 to MN7.11)	58	0	29-Mar-18 A	18-May-19 A		Road Drainage and Pavement (near NB67-2, MN7.9 to MN7.11)					
FHW-2350b	Installation of Drain pipe and Manholes (MN7.12 & MN7.12A) (affected by Tau Pass under VO191)	29	0	26-Nov-18 A	23-Apr-19 A		Installation of Drain pipe and Manholes (MN7.12 & MN7.12A) (affected by Tau Pass under VO191)					
FHW-2350c	Road Drainage and Pavement (near NB67-2, MN7.12 & MN7.12A) (affected by Tau Pass, VO not yet issued)	46	0	20-Jan-19 A	13-May-19 A		Road Drainage and Pavement (near NB67-2, MN7.12 & MN7.12A) (affected by Tau Pass, VO not yet issued)					
Fanling Highway Zone 3 between CH7290 and CH7380												
Noise Barrier												
FHW-3340	Noise Barrier NB69 - Pile cap/ Footing and Stem Wall adjacent to NB lane (108m)	77	0	16-Oct-17 A	30-Apr-19 A		Noise Barrier NB69 - Pile cap/ Footing and Stem Wall adjacent to NB lane (108m)					
At-Grade Roadworks (130m)												
FHW-3240	Road Pavement on FLH SB 4th lane after Removal of Temp. Street Light (due to Claim No. 63)	10	10	31-Aug-18 A	30-May-19	296	Road Pavement on FLH SB 4th lane after Removal of Temp. Street Light (due to Claim No. 63), Road Drainage (FLH NB hard shoulder, next to NB69)					
FHW-3350a	Road Drainage (FLH NB hard shoulder, next to NB69)	61	0	26-Feb-18 A	18-May-19 A		Road Drainage (FLH NB hard shoulder, next to NB69)					

- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- ◆ Milestone
- Project Baseline Bar

CEDD Contract No. CV/2012/09
Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3
3-Month Rolling Programme
3MPR070 _____ **Page 1 of 5** _____ **20-May-19**


3-Month Rolling Programme			
Date	Revision	Checked	Approved
20-May-19	Revision 0	FC	DH

Activity ID	Activity Name	OD	RD	Start	Finish	TF	2019						
							Mar	Apr	May	Jun	Jul	Aug	
FHW-3350b	Road Formation and Pavement (FLH NB 1st lane and HS next to NB69, due to Tau Pass under VO191)	25	0	19-Mar-19 A	16-May-19 A								
Fanling Highway North Portion between CH7470 and CH7925													
Fanling Highway Zone 4 between CH7380 and CH7470													
At-Grade Roadworks (90m)													
FHW-4150	Road Pavement (FLH SB 1st lane) by re-surfacing (due to Claim No. 63)	15	0	10-Sep-18 A	27-Apr-19 A								
FHW-4150a	Road Drainage and Road Pavement (FLH H.S., Merging Lane)(due to Claim No. 63)	48	0	10-Sep-18 A	16-Apr-19 A								
FHW-4330c	Construction of FL/RW2 (mass concrete wall, VO not yet received)	38	0	27-Aug-18 A	04-Apr-19 A								
FHW-4330d	Remaining Gullies and Road Pavement after Construction of FL/RW2 (VO not yet received)	25	0	11-Feb-19 A	18-May-19 A								
FHW-4330e	Road Drainage MN9.1 - MN9.3	24	0	23-Aug-18 A	20-May-19 A								
Fanling Highway Zone 5 between CH7470 and CH7600 (Provision of Kiu Tau Footbridge)													
Kiu Tau Footbridge Re-provision (East)													
FHW-5070	Installation of Lighting Facilities (affect by design change which is under VO)	21	46	20-Jun-18 A	13-Jul-19	260							
FHW-5090	Erection of Pillar Box (affect by design change which is under VO)	30	0	28-Feb-19 A	29-Mar-19 A								
FHW-5100	Power Cable Laying Works (affect by design change which is under VO)	36	36	20-May-19*	02-Jul-19	233							
FHW-5110	Permanent Power Supply Connection (affect by design change which is under VO)	10	10	03-Jul-19	13-Jul-19	260							
FHW-5110a	Installation of Drainage Pipe	32	22	10-Sep-18 A	14-Jun-19	284							
FHW-5110b	Laying of Floor Tiles (affect by design change which is under VO)	72	12	28-Jun-18 A	01-Jun-19	294							
FHW-5110c	Installation of Suspended Ceiling (affect by design change which is under VO)	104	12	21-May-18 A	01-Jun-19	294							
Provision of BFA Facilities (Lift)													
FHW-L-104f	Permanent Power Supply (affect by design change which is under VO)	10	10	03-Jul-19*	13-Jul-19	233							
FHW-L-106f	Testing & Commissioning (affect by design change which is under VO)	27	27	15-Jul-19*	14-Aug-19	233							
Works at existing TWSRE													
FHW-5490	Road Drainage, Pavement and TCSS duct laying (Merging lane next to NB72)(due to claim)	2	2	25-May-19*	27-May-19	299							
FHW-5500	Road Drainage (MS10.1-10.3A), Road Pavement and TCSS duct laying (Merging lane next to NB73)	31	44	21-Apr-18 A	11-Jul-19	262							
At-Grade Road Works (130m)													
FHW-5130	Road Pavement (FLH SB 1st lane) by re-surfacing (due to claim 63)	15	18	10-Sep-18 A	10-Jun-19	288							
FHW-5330a	Road Drainage (MN10.1-10.3A, gullies affected by Slope F18)	60	15	16-Dec-17 A	05-Jun-19	291							
FHW-5330c	Fill Replacement Works 3SW-DF18 next to FLH NB (further modified by VO not yet received)	73	24	01-Aug-18 A	17-Jun-19	282							
FHW-5330d	Remaining Gullies, road formation and TCSS duct laying (log on effect by Slope F18 under VO)	25	0	23-Jan-19 A	26-Mar-19 A								
FHW-5330e	Road Pavement (log on effect by Slope F18 under VO)	14	14	20-May-19*	04-Jun-19	292							
Fanling Highway Zone 6 between CH7600 and CH7660 (Existing Vehicular Bridge)													
At-Grade Roadworks (60m)													
FHW-6330a	Road Drainage and Road Formation (FLH NB hard shoulder)	60	18	16-Dec-17 A	10-Jun-19	288							
Fanling Highway Zone 7 between CH7660 and CH7925 at NBZ (Section 1B)													

- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- ◆ Milestone
- Project Baseline Bar

CEDD Contract No. CV/2012/09
Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3
3-Month Rolling Programme
 3MPR070 _____ Page 2 of 5 _____ 20-May-19

3-Month Rolling Programme			
Date	Revision	Checked	Approved
20-May-19	Revision 0	FC	DH

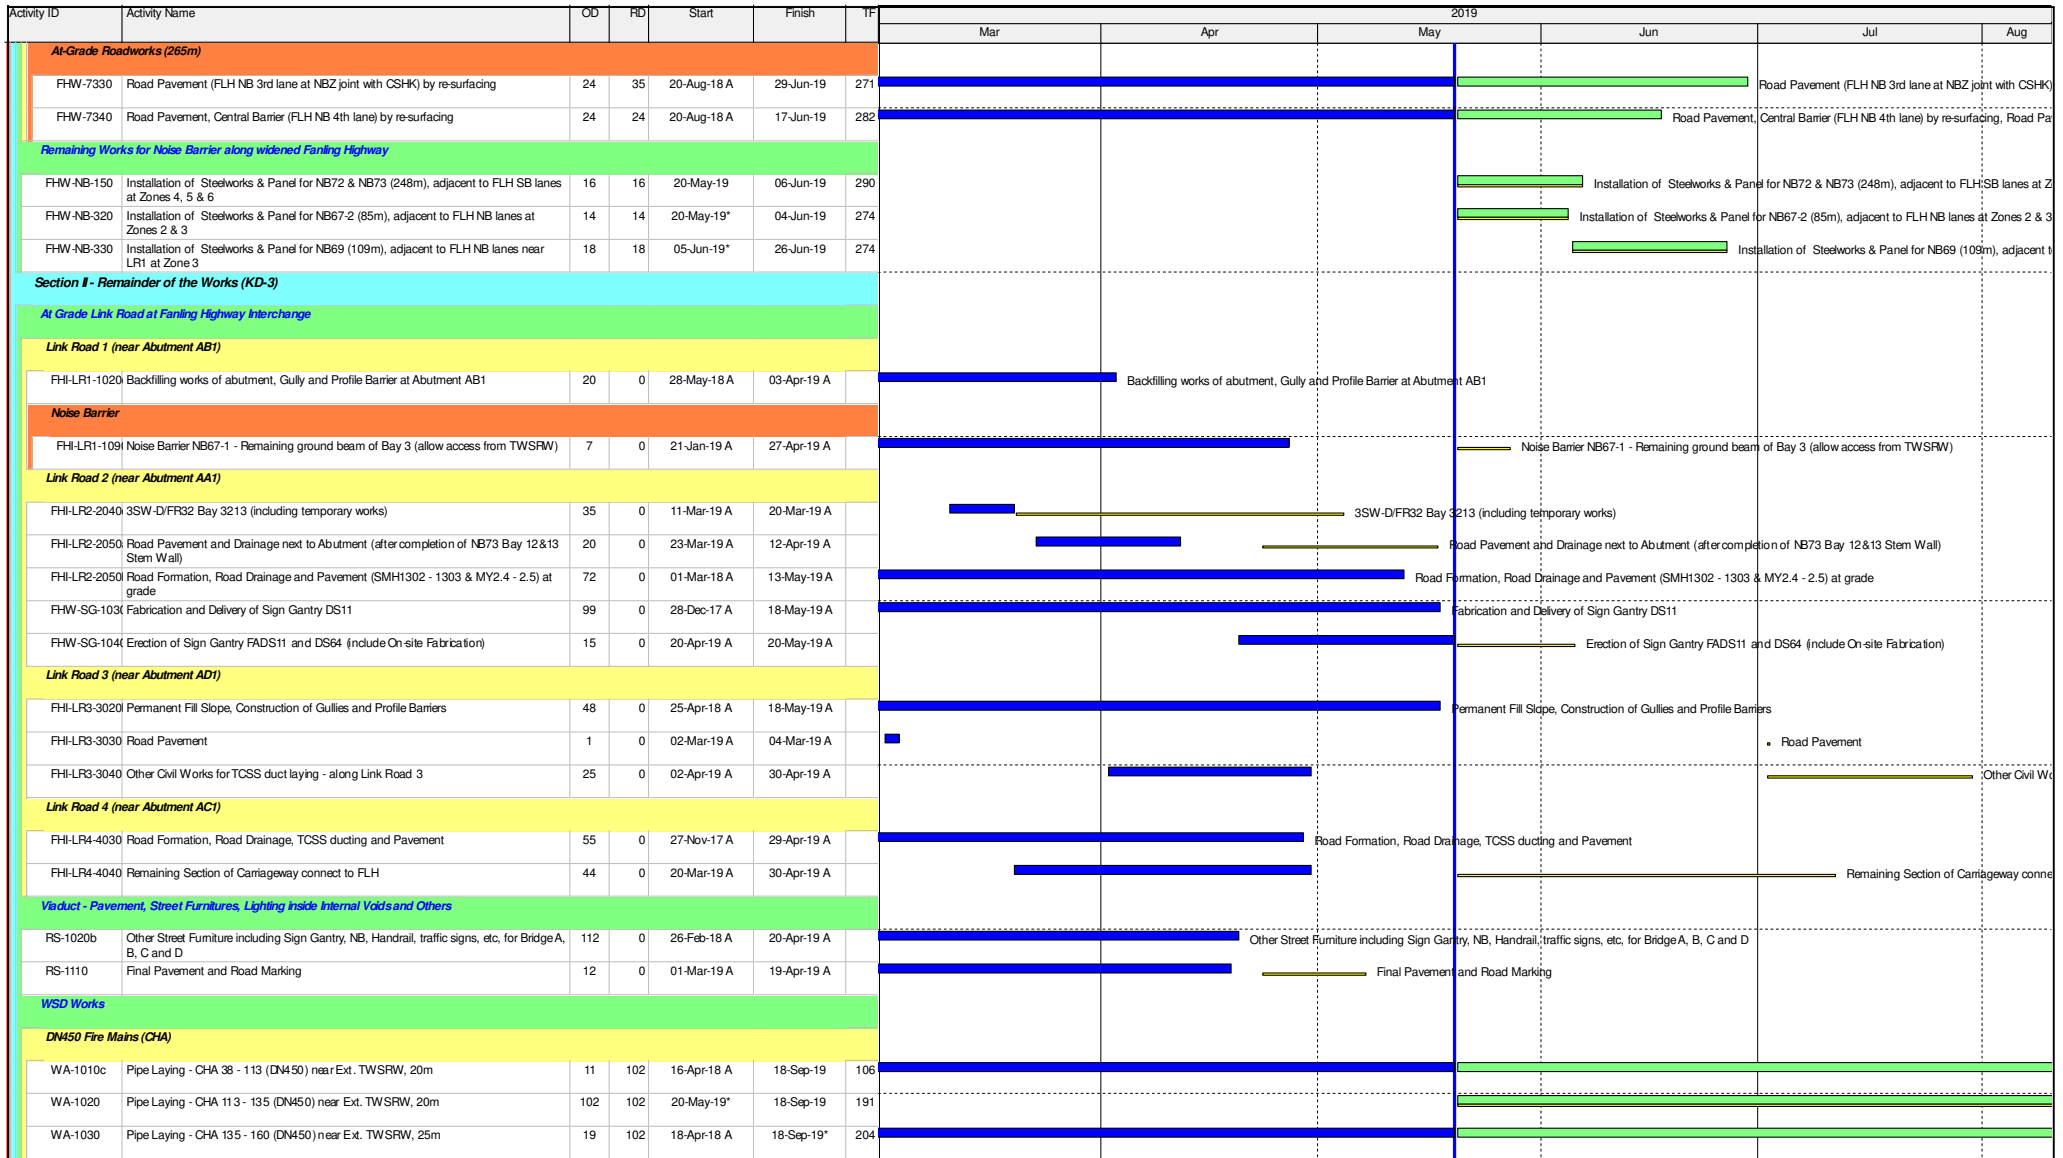

- Actual Work
- Remaining Work
- Summary Bar
- Critical Remaining Work
- ◆ Milestone
- Project Baseline Bar

CEDD Contract No. CV/2012/09
Liantang / Heung Yuen Wai BCP - Site Formation & Infrastructure Works, Contract 3
3-Month Rolling Programme
 3MPR070 _____ Page 3 of 5 _____ 20-May-19

3-Month Rolling Programme			
Date	Revision	Checked	Approved
20-May-19	Revision 0	FC	DH

