

# Appendix C Calibration Certificates of Monitoring Equipment



TISCH ENVIRONMENTAL, INC. 145 SOUTH MIAMI AVE VILLAGE OF CLEVES, OH 45002 513.467.9000 877.263.7610 TOLL FREE 513.467.9009 FAX

#### ORIFICE TRANSFER STANDARD CERTIFICATION WORKSHEET TE-5025A

Date - Ap		Rootsmeter Orifice I.I		438320 1612	Ta (K) - Pa (mm) -	294 - 742.95
PLATE OR Run #	VOLUME START (m3)	VOLUME STOP (m3)	DIFF VOLUME (m3)	DIFF TIME (min)	METER DIFF Hg (mm)	ORFICE DIFF H2O (in.)
1 2 3 4 5	NA NA NA NA NA	NA NA NA NA NA	1.00 1.00 1.00 1.00	1.3940 0.9790 0.8800 0.8350 0.6910	3.2 6.4 7.8 8.8 12.7	2.00 4.00 5.00 5.50 8.00

#### DATA TABULATION

				Va	(x axis) Qa	(y axis)
0.9866 0.9823 0.9804 0.9791 0.9739	0.7077 1.0034 1.1140 1.1726 1.4094	1.4077 1.9908 2.2258 2.3345 2.8155		0.9957 0.9914 0.9894 0.9881 0.9829	0.7142 1.0127 1.1243 1.1834 1.4224	0.8896 1.2581 1.4066 1.4753 1.7793
Qstd slope intercept coefficier	(b) = nt (r) =	2.00757 -0.01628 0.99989 	1 0 11	Qa slope intercept coefficie	= (b) $=$	1.25710 -0.01029 0.99989

## CALCULATIONS

Vstd = Diff. Vol[(Pa-Diff. Hg)/760](298/Ta)
Qstd = Vstd/Time

Va = Diff Vol [(Pa-Diff Hg)/Pa]
Qa = Va/Time

For subsequent flow rate calculations:

Qstd =  $1/m\{ [SQRT (H2O (Pa/760) (298/Ta))] - b\}$ Qa =  $1/m\{ [SQRT H2O (Ta/Pa)] - b\}$ 

#### TSP Sampler Calibration

#### SITE

Location: Lian Tang 3
Sampler: TE-5170 MFC (Serial # : 2359) Date: January 5, 2015 Tech: Sam Wong

CONDITIONS Barometric Pressure (in Hg): 39.95 Corrected Pressure (mm Hg): 1015 Temperature (deg F): Temperature (deg K): 292 Average Press. (in Hg): 39.95 Corrected Average (mm Hg): 1015 Average Temp. (deg F): Average Temp. (deg K):

#### CALIBRATION ORIFICE

Make: Tisch Qstd Slope: 2.00757 TE-5025A Qstd Intercept: -0.01628 Model: April 7, 2014 Serial#: 1612 Date Certified:

	CALIBRATIONS					
Plate or Test #	H2O (in)	Qstd (m3/min)	I (chart)	IC (corrected)	LINEAR REGRESSION	
1	12.00	2.023	58.0	67.72	Slope =	34.1786
2	10.00	1.847	54.0	63.05	Intercept =	-0.9409
3	8.20	1.673	48.0	56.04	Corr. coeff.=	0.9992
4	5.20	1.334	38.0	44.37		
5	3.20	1.048	30.0	35.03	# of Observations:	5

#### Calculations

Qstd = 1/m[Sqrt(H2O(Pa/Pstd)(Tstd/Ta))-b]

IC = I[Sqrt(Pa/Pstd)(Tstd/Ta)]

Qstd = standard flow rate

IC = corrected chart response

I = actual chart response m = calibrator Qstd slope

b = calibrator Qstd intercept

Ta = actual temperature during calibration (deg K)

Pa = actual pressure during calibration (mm Hg)

Tstd = 298 deg K

Pstd = 760 mm Hg For subsequent calculation of sampler flow:


1/m((I)[Sqrt(298/Tav)(Pav/760)]-b)

= sampler slope = sampler intercept m

b

= chart response

Tav = daily average temperature Pav = daily average pressure

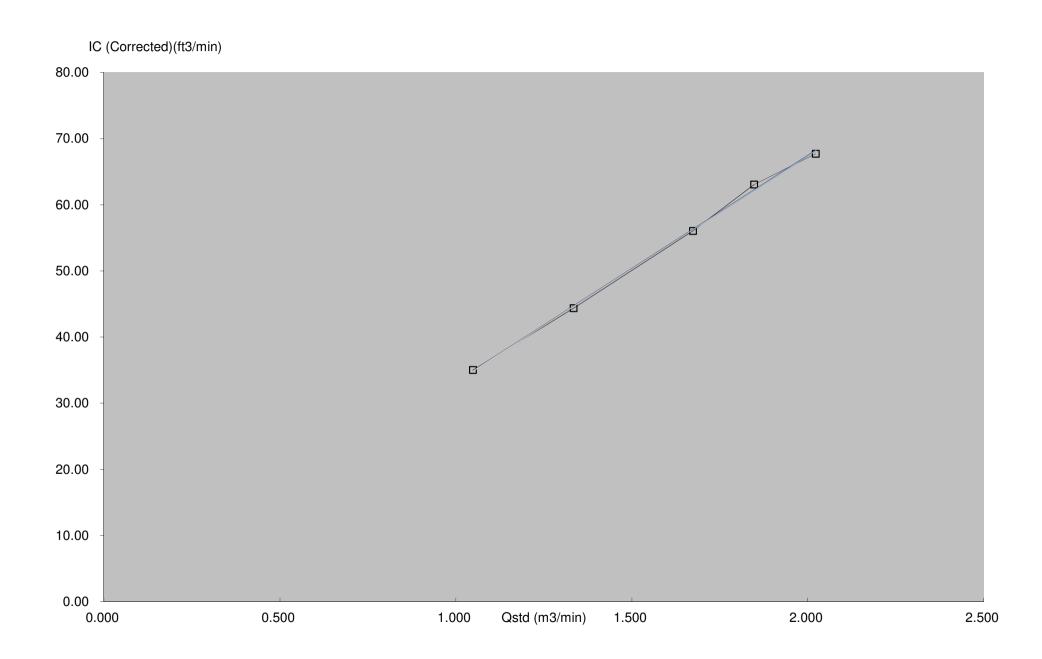



Certificate No. 407497

2 Pages 1 of Page

Customer: Enovative Environmental Service Limited

Address: Flat 6, 3/F, Block E, Wah Lok Industrial Centre, 31-35 Shan Mei Street, Shatin, N.T., Hong Kong.

Order No.: Q43167

Date of receipt

**Item Tested** 

Description : Sound Level Calibrator

Manufacturer: B&K

Model : Type 4231 Serial No.

: 2685684

**Test Conditions** 

Date of Test: 18-Oct-14 Ambient Temperature :

Supply Voltage : --

Relative Humidity: (50 ± 25) %

**Test Specifications** 

Calibration check.

Ref. Document/Procedure: F21, Z02, IEC 942.

#### **Test Results**

All results were within the IEC 942 Class1 specification.

 $(23 \pm 3)^{\circ}C$ 

The results are shown in the attached page(s).

Main Test equipment used:

-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI). The test results apply to the above Unit-Under-Test only

Calibrated by :

Approved by:

18-Oct-14

Date:

Steve Kwan

This Certificate is issued by

Hong Kong Calibration Ltd.

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong

Tel: 2425 8801 Fax: 2425 8646

The copyright of this certificate is owned by Hong Kong Calibration Ltd.. It may not be reproduced except in full



Certificate No. 407497

Page 2 of 2 Pages

Results:

## 1. Level Accuracy

UUT Nominal Value (dB)	Measured Value (dB)	IEC 942 Class 1 Spec.
94	94.1	± 0.3 dB
114	114.1	

Uncertainty: ± 0.1 dB

#### 2. Frequency

UUT Nominal Value	Measured Value	IEC 942 Class 1 Spec.
1 kHz	1.000 kHz	± 2 %

Uncertainty:  $\pm 3.6 \times 10^{-6}$ 

3. Level Stability: 0.0 dB

IEC 942 Class 1 Spec. : ± 0.1 dB

Uncertainty: ± 0.01 dB

4. Total Harmonic Distortion : < 0.6 %

IEC 942 Class 1 Spec. : < 3 % Uncertainty : ± 2.3 % of reading

Remark: 1. UUT: Unit-Under-Test

2. The uncertainty claimed is for a confidence probability of not less than 95%.

3. Atmospheric Pressure: 1005 hPa.

----- END -----



Certificate No. 406516

Page 1 of 4 Pages

Customer: Enovative Environmental Service Limited

Address: Flat 6, 3/F, Block E, Wah Lok Industrial Centre, 31-35 Shan Mei Street, Shatin, N.T., Hong Kong.

Order No.: 042822

Date of receipt : 1-Sep-14

**Item Tested** 

Description : Sound Level Meter (N12-RION-004)

Manufacturer: Rion

Model : NL-52

Serial No.

: 00220553

**Test Conditions** 

Date of Test: 24-Sep-14

Supply Voltage : --

.

Ambient Temperature: (

 $(23 \pm 3)^{\circ}C$ 

Relative Humidity: (50 ± 25) %

**Test Specifications** 

Calibration check.

Ref. Document/Procedure: Z01, IEC 61672.

#### **Test Results**

All results were within the IEC 61672 Type1 specification.

The results are shown in the attached page(s).

Main Test equipment used:

Equipment No. Description

Cert. No.

Traceable to

S017

Multi-Function Generator

C127181

SCL-HKSAR

S205

Ref. Sound Level Calibrator

PHCO40002

SCL-HKSAR

The values given in this Calibration Certificate only relate to the values measured at the time of the test and any uncertainties quoted will not include allowance for the equipment long term drift, variations with environmental changes, vibration and shock during transportation, overloading, mis-handling, or the capability of any other laboratory to repeat the measurement. Hong Kong Calibration Ltd. shall not be liable for any loss or damage resulting from the use of the equipment.

The test equipment used for calibration are traceable to International System of Units (SI). The test results apply to the above Unit-Under-Test only

Calibrated by :

Dorothy Cheuk

Approved by:

Steve Kwan

This Certificate is issued by:

Hong Kong Calibration Ltd.

\_\_\_\_\_

25-Sep-14

Unit 8B, 24/F., Well Fung Industrial Centre, No. 58-76, Ta Chuen Ping Street, Kwai Chung, NT, Hong Kong. Tel: 2425 8801 Fax: 2425 8646

Certificate No. 406516

Page 2 of 4 Pages

Results:

1. Self-generated noise: 16.0 dBA (Mfr's Spec ≤ 17 dBA)

2. Acoustical signal test

	UUT S	etting			
Range (dB)	Frequency Weighting	Time Weighting	Octave Filter	Applied Value (dB)	UUT Reading (dB)
30-130	A	F	OFF	94.2	94.2
		S	OFF		94.2
	С	F	OFF		94.2
	Z	F	OFF		94.2
	A	F	OFF	114.2	114.2
		S	OFF		114.2
	С	F	OFF		114.2
	Z	F	OFF		114.2

IEC 61672 Type 1 Spec. : ± 1.1 dB

Uncertainty: ± 0.1 dB

## 3 Electrical signal tests of frequency weightings (A weighting)

Frequency	Attenuation (dB)	IEC 61672 Type 1 Spec.
31.5 Hz	-39.7	- 39.4 dB, ± 2 dB
63 Hz	-26.3	- 26.2 dB, ± 1.5 dB
125 Hz	-16.2	- 16.1 dB, ± 1.5 dB
250 Hz	-8.7	- 8.6 dB, ± 1 dB
500 Hz	-3.2	- 3.2 dB, ± 1.4 dB
1 kHz	0.0 (Ref)	0 dB, ± 1.1 dB
2 kHz	+1.2	+ 1.2 dB, ± 1.6 dB
4 kHz	+1.0	+ 1.0 dB, ± 1.6 dB
8 kHz	-1.0	$-1.1 \text{ dB}, +2.1 \text{ dB} \sim -3.1 \text{ dB}$
16 kHz	-8.0	- 6.6 dB, + 3.5 dB ~ - 17.0 dB

Uncertainty:  $\pm 0.1 dB$ 



Certificate No. 406516

Page 3 of 4 Pages

## 4. Frequency & Time weightings at 1 kHz

4.1 Frequency Weighting (Fast)

UUT	Applied	UUT	Difference	IEC 61672
Setting	Value (dB)	Reading (dB)	(dB)	Type 1 Spec.
A	94.2	94.2 (Ref.)	(45)	± 0.4 dB
C	94.2	94.2	0.0	± 0.4 dB
Z	94.2	94.2	0.0	

4.2 Time Weighting (A-weighted)

UUT	Applied	UUT	Difference	IEC 61672
Setting	Value (dB)	Reading (dB)	(dB)	Type 1 Spec.
Fast	94.2	94.2 (Ref.)		± 0.3 dB
Slow	94.2	94.2	0.0	
Time-averaging	94.2	94.2	0.0	

Uncertainty: ± 0.1 dB

## 5. Level linearity on the reference level range

	Applied			
UUT Range	Value (dB)	UUT Reading (dB)	Difference (dB)	IEC 61672 Type 1 Spec.
30-130 dB	129.0	129.0	0.0	± 1.1 dB
(Ref Level)	124.0	124.0	0.0	
	119.0	119.0	0.0	
	114.0	114.0 (Ref)		
	109.0	109.0	0.0	
	104.0	104.0	0.0	
	99.0	99.0	0.0	
	94.0	94.0	0.0	
	89.0	89.0	0.0	
	84.0	84.0	0.0	
	79.0	79.0	0.0	
	74.0	74.0	0.0	F
	69.0	69.0	0.0	
	64.0	64.0	0.0	
	59.0	59.0	0.0	
	54.0	54.0	0.0	
	49.0	49.1	+0.1	
	44.0	44.1	+0.1	

Uncertainty: ± 0.1 dB



Certificate No. 406516

Page 4 of 4 Pages

## 6. Toneburst response (4kHz)

UUT	Tone Burst	UUT	Difference	IEC 61672
Setting	Duration(ms)	Reading(dB)	(dB)	Type 1 Spec.
Fast	Steady	127.0(Ref)		
	200	126.0	-1.0	$-1.0 \pm 0.8$ dB
	2	109.0	-18.0	$-18.0$ , $+1.3 \text{ dB} \sim -1.8 \text{ dB}$
	0.25	99.9	-27.1	-27.0, +1.3 dB ~ -3.3 dB
Slow	Steady	127.0(Ref)		
	200	119.6	-7.4	$-7.4 \pm 0.8$ dB
	2	100.0	-27.0	-27.0, +1.3 dB ~ -3.3 dB
Time	Steady	127.0(Ref)		
averaging	200	120.4	-6.6	-7.0±0.8dB
	2	100.3	-26.7	-27.0, +1.3 dB ~ -1.8 dB
	0.25	91.0	-36.0	-36.0, +1.3 dB ~ -3.3 dB

Uncertainty: ± 0.1 dB

## 7. Overload indication (30-130 dB range, A-weighted, Time-average, 4kHz)

UUT Reading at overload (dB)			
+ ve one half cycle	- ve one half cycle	Difference (dB)	IEC 61672 Type 1 Spec.
136.1	137.2	1.1	< 1.8 dB

The overload indicator latched on until reset

Uncertainty: ± 0.1 dB

Remarks: 1. UUT: Unit-Under-Test

- 2. The uncertainty claimed is for a confidence probability of not less than 95%.
- 3. Atmospheric Pressure: 1001 hPa.
- 4. Preamplifier model: NH-25, S/N: 10553
- 5. Firmware Version: 1.2
- 6. Power Supply Check: OK
- 7. The UUT was adjusted with the laboratory's sound calibrator at the reference sound pressure level before the calibration.

	END	
THE NEW YOR THE THE WAY WAS NOT THE THE		
